



Implementation Approach and Plan for BrokerVerse OOTB

Prepared by – **iorta TechNXT**

Version – **1.1**

Date – **04 October 2026**

TABLE OF CONTENTS

1. Document Control.....	4
2. Acronyms.....	4
3. Introduction.....	5
3.1 Purpose.....	5
3.2 Companion documents.....	5
3.3 Audience.....	6
3.4 Version history.....	6
4. Implementation approach.....	7
4.1 Configure, do not customise.....	7
4.2 Principles.....	8
4.3 Implementation sizes.....	8
4.4 Environment model.....	9
5. Phases.....	10
5.1 Overview.....	10
5.2 Mobilisation.....	11
5.3 Environments and pipeline.....	12
5.4 Discovery and fit-gap.....	12
5.5 Client inputs and the configuration kit.....	13
5.6 Regulatory registrations.....	13
5.7 Configuration.....	14
5.8 Compliance set-up.....	14
5.9 Branding and brand pack.....	15
5.10 Data migration.....	15
5.11 Integrations with partners.....	15
5.12 Training.....	16
5.13 System integration test.....	16
5.14 User acceptance test.....	16
5.15 Rehearsal, cutover and go-live.....	17
5.16 Hypercare.....	17
6. Timelines by size.....	18
6.1 Phases and milestones.....	18
6.2 Small broker (8 weeks).....	19
6.3 Medium broker (12 weeks).....	20
6.4 Large broker (20 weeks).....	21
6.5 Enterprise broker (26 weeks).....	22
6.6 Task-level plan.....	23

7. Roles and responsibilities.....	25
7.1 Project roles.....	25
7.2 RACI.....	25
8. Governance.....	27
8.1 Steering committee.....	27
8.2 Weekly status.....	27
8.3 RAID log.....	27
9. Deliverables and acceptance criteria.....	28
10. Assumptions.....	29
11. Exclusions.....	30
12. Dependencies on the broker.....	31
13. Risks and mitigations.....	32
14. Change request process.....	33
15. Document Sign-Off.....	34

1. Document Control

Date	Version	Author & Business Unit Info	Reviewed By & Business Unit Info	Approved By & Business Unit Info	Change History
04 October 2026	1.1	iorta TechNXT			Four broker sizes with the environment model; go-live configuration and migration kits; compliance set-up, branding, partner integrations and regulatory registrations as phases; task-level plan from one model

2. Acronyms

Acronym / Symbol	Definition / Meaning
OOTB	Out of the box
AMLC	Anti-Money Laundering Council
ATP	Authority to Print
BIR	Bureau of Internal Revenue
CAS	Computerized Accounting System
COC	Certificate of cover
CoA	Chart of accounts
CR	Change request
CTPL	Compulsory Third Party Liability
Dev	Development environment
DPO	Data protection officer
EIS	Electronic Invoicing System
GL	General ledger

IC	Insurance Commission
LTO	Land Transportation Office
NPC	National Privacy Commission
PM	Project manager
Pre-Prod	Pre-production environment
RACI	Responsible, Accountable, Consulted, Informed
RAID	Risks, Assumptions, Issues, Dependencies
SIT	System integration test
SMTP	Simple Mail Transfer Protocol
SteerCo	Steering committee
TTT	Train the trainer
UAT	User acceptance test

3. Introduction

3.1 Purpose

This document describes how iorta TechNXT implements BrokerVerse OOTB for a Philippine non-life insurance broker: the approach, the phases, a week-by-week plan for small, medium, large and enterprise brokers, who does what, how the project is governed, what each phase delivers and how it is accepted, and what is in and out of scope.

3.2 Companion documents

Document	What it adds
BrokerVerse_Implementation_Plan.xlsx	The task-level plan of each size: duration, owner party (iorta TechNXT, broker or partner),

Document	What it adds
	owner role, deliverable, predecessors, dates from the kick-off date, float and critical path; the milestones; every link; the full RACI
BrokerVerse Dependency Map and Critical Path	Diagrams of the dependencies (client inputs, partner certifications, regulatory registrations, environments and keys), the critical path and lead times by size, and what slips when a dependency slips
BrokerVerse_RAID_Log_Template.xlsx	The RAID log, pre-filled with the risks, assumptions, issues and dependencies typical of an implementation
BrokerVerse Data Migration and Cutover Plan	Data objects, templates, load sequence, reconciliation, cutover and rollback
BrokerVerse Environment Strategy and Production Rollout	Environment sets, release pipeline, promotion of configuration, cutover runbook T-30 to T+30
BrokerVerse Training Plan	Training per role, including the compliance officer, curriculum, train-the-trainer, assessment
BrokerVerse Philippine Regulatory Compliance Matrix	How the system supports the broker's IC, BIR, AMLA and Data Privacy Act obligations
BrokerVerse User Manual	Every screen, for every role
Go-live data set-up and workbench (docs/onboarding/GO_LIVE_DATA_SETUP.md, GO_LIVE_DATA_WORKBENCH.md)	The order of set-up and the use of the configuration and migration kits
Release pipeline and deployment (deploy/RELEASE_PIPELINE.md, deploy/README.md, deploy/REFERENCE.md)	GitHub Environments, secrets, deployment, rollback, key rotation

The plan tables of this document, the workbook and the diagrams come from one plan model (docs/package/tools/delivery/plan_model.py), so they agree.

3.3 Audience

The broker's management (sponsor and steering committee), the broker's project manager, the process owners of Sales, Placement and Policy Processing, Client Servicing, Claims and Accounting, the broker's compliance officer and data protection officer, the broker's IT or System Administrator, and the iorta TechNXT head of delivery, project manager and project team.

3.4 Version history

Version	Date	Change
1.0	03 October 2026	Initial issue: three sizes, twelve phases, RACI, governance, deliverables
1.1	04 October 2026	Four sizes (enterprise added) with the environment model; configuration through the go-live configuration kit and migration through the migration kit; new phases for compliance set-up (AML/CFT, IC and NPC registers, masking), branding and the brand pack, integrations with partners (banks, SMS, CTPL authentication and LTO, insurers, BIR EIS, AMLC reporting) and regulatory registrations; GitHub Environments and encryption keys in the environment phase; task-level plan with owners, predecessors and milestones; dependencies and risks aligned with the Dependency Map and the RAID log

4. Implementation approach

4.1 Configure, do not customise

BrokerVerse OOTB is a finished product for Philippine non-life broking. It covers the broking cycle from lead to renewal (leads and their assignment, quotations, requests for quotation, placement slips, cover notes, policy issue, endorsements, cancellations, claims with document checklists and motor repairs, renewals), distribution (channels, dealer programmes, fleets, marine open covers, facultative placements, campaigns), the accounting of a broker (billing, instalments, official receipts and sales invoices, post-dated cheques, collections, remittance to insurers, direct bill, commission and insurer overrides, payables, fixed assets, petty cash, journals, bank reconciliation and bank payment files, month-end and year-end close), the BIR forms and files (2307, 0619-E, 1601-EQ, 1604-E, 2551Q, DAT files, EOPT invoices, EIS connector, CAS books), AML/CFT, the IC and NPC registers, and the integration framework (SMS, CTPL authentication, insurer APIs, bank files). The implementation fits the broker to the product through configuration and master data. It does not change the code.

What the broker sets without code:

Area	Where in BrokerVerse
Company, letterhead, branches, departments	Master > Organization; Master > System Configuration > System Settings
Theme, logo, sign-in picture, branded documents and e-mails, e-signatures, brand packs	Master > System Configuration > System Settings > Theme and Branding; Signatories; My Profile > My e-signature
Users, roles, reporting lines, authority limits	Master > User Management (User, Role, User Access Matrix, Role Permissions, Authority Matrix, Delegations, Segregation of Duties, Access Reviews); Master > Employee Management > Hierarchy
Philippine addresses	Master > Location (Country, Province, City / Municipality; regions and barangays from the PSGC)
Insurers, lines of business, products, covers, vehicles, distribution channels	Master > Insurance Management
Product templates, rating factors, acceptance rules (refer, decline, loading with authority), document templates with merge fields, market and risk mapping	Product Configurator
Commission rates, premium taxes and LGU rates, tax codes with ATC, chart of accounts, account determination, posting rules	Master > Finance
Banks, bank accounts, statement formats, bank file layouts, payment gateways	Master > Finance
Document numbering, business rules, limits, maker-checker switches, security, go-live settings	Master > System Configuration > Document Numbering, Configuration
Scheduled jobs; connectors, message templates, insurer mappings	Master > System Configuration > Schedules, Integrations, Message Templates, Insurer Integration
AML/CFT settings, risk factors, monitoring rules, screening lists	Compliance > AML Settings, Screening Lists
IC licences, fit and proper, insurer authority, complaints, breach register	Compliance > Insurance Commission; Compliance > Data Privacy (NPC)
Masking of personal identifiers by role	Role permission view:pii; settings privacy.masking_enabled, privacy.pii_reveal_mode

A requirement that cannot be met by configuration, master data or a change in the broker's procedure is a gap. Gaps are recorded in the fit-gap register and handled through the change request process (chapter Change request process). They do not enter the go-live scope unless the steering committee approves them as a change request.

4.2 Principles

- **Product first.** The process walk-throughs use the delivered screens with the broker's own examples. The broker adapts a procedure before anyone asks for a change.
- **Data drives the timeline.** The insurer, product and commission data and the chart of accounts are on the critical path for every size. Requests for data and the blank kits go out in week 1.
- **Two kits, loaded again and again.** Configuration moves through the configuration kit and migration through the migration kit (Master > Go-Live and Data > Go-Live Data Load): validate as a trial run, correct with the errors workbook, load, and load again without duplicates. The same kit promotes configuration from Dev or SIT to UAT and Production.
- **Key users own the result.** Each team names one key user who takes part in discovery, tests the configuration, runs UAT and trains the team.
- **Registrations start on day one.** BIR, AMLC, NPC and IC items have lead times outside the project's control; they are confirmed or started at kick-off.
- **Partners certify, the product waits in test mode.** Every connector works in test mode until the partner certifies it; a partner that is late does not stop the go-live when a fallback exists.
- **Evidence for every acceptance.** Each phase ends with named deliverables and acceptance criteria. Sign-off is written.

4.3 Implementation sizes

The size follows the number of named users, as in the Service Catalogue and Rate Annex. The other figures are a typical profile (assumption); the steering committee confirms the size at mobilisation once the data volumes are known.

Size	Named users	Typical profile (assumption)	Environments	Duration to hypercare exit	Go-live
Small	1 to 25	One office, up to 10 insurers, up to 5,000 in-force policies	Dev, UAT, Production; Pre-Prod temporary	8 weeks	Start of week 7
Medium	26 to 100	Up to 3 offices, up to 25 insurers, up to 25,000 in-force policies, co-insurance	Dev, UAT, Production; Pre-Prod temporary	12 weeks	Start of week 10
Large	101 to 300	Several branches, many insurers, more than 25,000 in-force policies, several bank accounts, referrer networks	Dev, SIT, UAT, Production with high availability; Pre-Prod temporary	20 weeks (16-week variant possible)	Start of week 15
Enterprise	Above 300	National network, bank-affiliated or group broker, dealer programmes and fleets	As large, with a cross-region copy of the backups	26 weeks, planned at mobilisation	Start of week 21

An import file holds at most 20,000 data rows (IMPORT_MAX_ROWS). Larger books are loaded in several files, which the large and enterprise plans allow for.

4.4 Environment model

The environment set follows the broker size (decision of the product owner, 04 October 2026).


Size	Where configuration is built and SIT runs	Where mock loads run	Where UAT and training run	Pre-Prod
Small and medium	Dev: configuration build, integration and system integration test with synthetic data only	UAT	UAT	Temporary: created from a production backup for the cutover rehearsal, removed after hypercare
Large and enterprise	Dev for development and integration; SIT for configuration, system integration test and the first mock loads	SIT, then UAT	UAT (separate from SIT)	Temporary, as above

One build is promoted unchanged through the environments by the release pipeline (ci.yml, deploy.yml, rollback.yml): Dev automatically from the integration branch, SIT by hand, UAT on a release candidate tag, Pre-Prod by hand, Production on a release tag with two approvers.

5. Phases

5.1 Overview

#	Phase	What happens
1	Mobilisation	Kick-off, team and governance, plan confirmed, data request and kits issued, hosting and environment set decided
2	Environments and pipeline	Dev, SIT (large, enterprise), UAT and Production; GitHub Environments with reviewers and secrets; application secrets and encryption keys with their custody; first deployment through the pipeline
3	Discovery and fit-gap	Process, compliance, integration and branding workshops on the delivered system; configuration decisions; fit-gap register
4	Client inputs	The broker fills the configuration kit, provides the partner contracts and prepares the migration extracts
5	Regulatory registrations	BIR ATP or CAS and EIS enrolment; AMLC registration; IC licence data; NPC registration; screening lists; tax adviser confirmation
6	Configuration	Configuration kit validated and loaded; on-screen configuration (Product Configurator, tax codes, posting rules, approvals, roles, schedules)
7	Compliance set-up	AML/CFT settings, risk factors and rules, screening lists; licence register, fit and proper, insurer authority; complaints and breach settings; masking by role
8	Branding and brand pack	Theme, letterhead, sign-in page, branded documents and e-mails, e-signatures mapped to documents, brand pack exported for promotion
9	Integrations with partners	E-mail; bank statement formats and bank payment files; SMS or Viber; CTPL authentication and LTO; insurer APIs; payment gateway; BIR EIS; AMLC report file
10	Data migration	Mapping to the migration kit, mock loads with reconciliation
11	Training	Train-the-trainer, compliance officer and DPO training, end-user training per role
12	SIT and UAT	System integration test in Dev or SIT; UAT with the broker's data; sign-off
13	Rehearsal and cutover	Release to Production; Pre-Prod from a production backup; rehearsal; go/no-go; cutover; go-live lock
14	Hypercare	Close support until the first month-end close; handover to production support

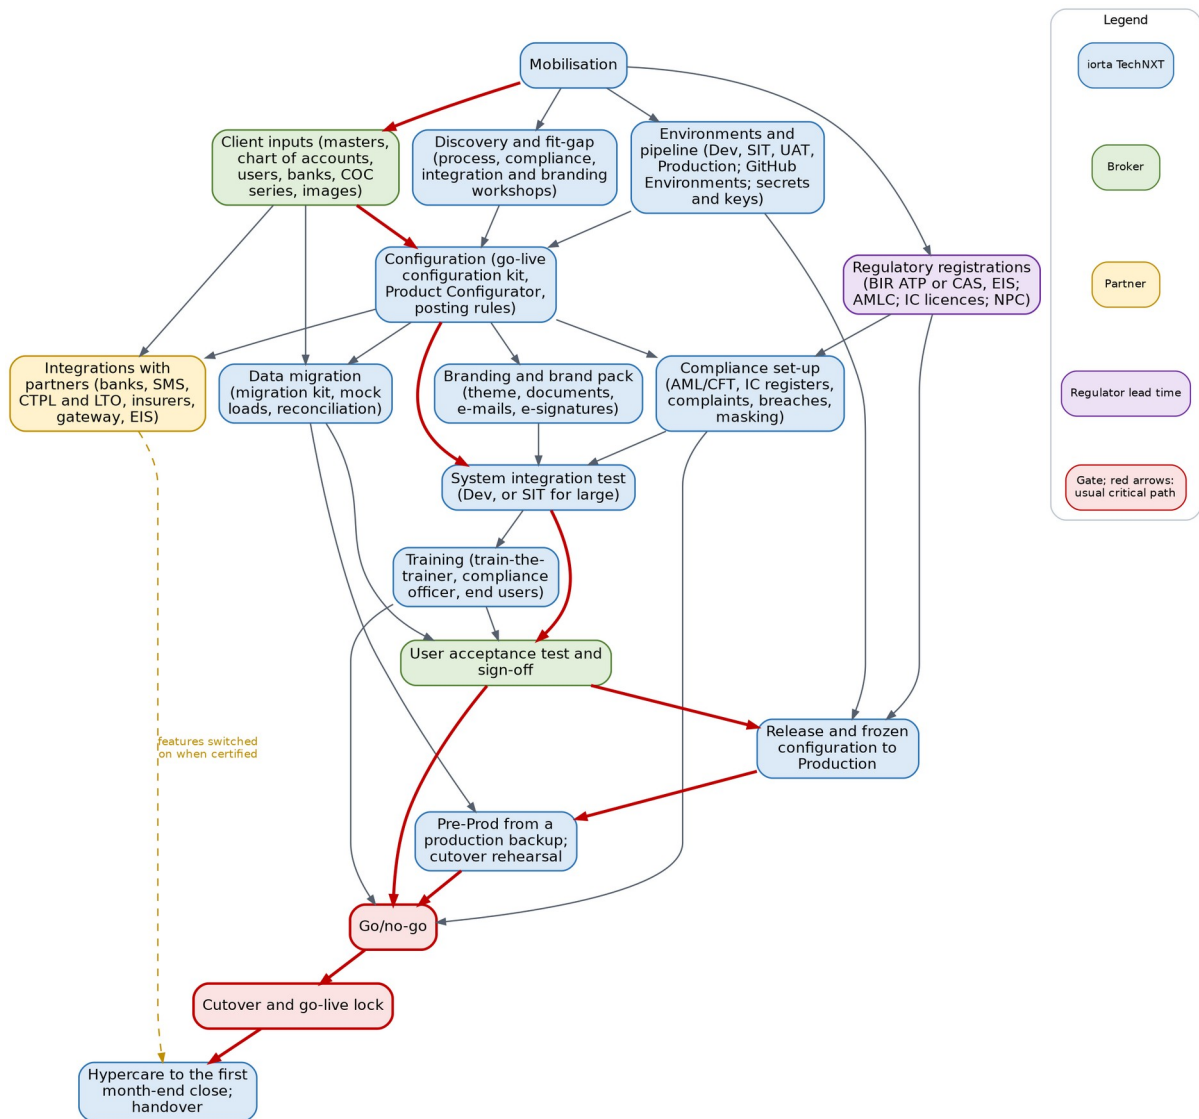

Dependencies between the phases. Red arrows: the usual critical path

5.2 Mobilisation

- Kick-off meeting with the sponsor, the broker's project manager, the key users, the compliance officer, the DPO and the iorta TechNXT team.
- Confirm the size, the plan, the go-live date and the hypercare window; baseline the plan workbook with the kick-off date.
- Set up the steering committee, the weekly status meeting and the RAID log, pre-filled from the template.
- Issue the data request list and the blank kits (configuration workbook, migration workbook, upload templates).
- Ask which registrations the broker already holds (ATP or CAS, AMLC registration, NPC registration, IC licences) and start the others the same day.
- Decide the hosting option, the environment set and the data location, including any transfer of personal data outside the Philippines.

5.3 Environments and pipeline

- iorta TechNXT provisions the environment set of the size following `deploy/README.md` and the Environment Strategy and Production Rollout: database time zone Asia/Manila, daily snapshots kept at least 30 days, health checks wired to monitoring, a restore test before go-live.
- **GitHub Environments** `dev`, `sit`, `uat`, `preprod` and `production` are set once by the repository owner: required reviewers on `uat`, `preprod` and `production` (`production`: two, prevent self-review), tag rules, variables (`DEPLOY_ENABLED`, `targets`, `addresses`, `environment name`) and environment secrets (`deploy keys`, `known hosts`, `bucket` and `distribution ids`). Repository-level secrets of the same names are removed.
- **Application secrets** live in the secret store of each environment, never in GitHub or the repository: `JWT_SECRET`, `DATA_ENCRYPTION_KEY`, `PII_ENCRYPTION_KEY` (each at least 32 characters and different from the others), `DATABASE_URL`, `SMTP_URL` and the partner credentials. The API refuses to start in `production` without them.
- **Key custody.** `PII_ENCRYPTION_KEY` encrypts TIN, government ID and bank account numbers; without it a backup cannot be read. The broker IT head and the iorta TechNXT DevOps lead sign a custody record: who holds the escrow copy under dual control, where it is kept with the backups, and the rotation procedure of `deploy/REFERENCE.md`.
- `Production` starts with reference data only (`SEED_SAMPLE_DATA=false`). `Dev` may carry the delivered sample data; `UAT` holds the broker's data from the first mock load and is then protected as `Production` is.

5.4 Discovery and fit-gap

Discovery is limited to configuration. Each workshop shows the delivered screens with the broker's own examples and records the decisions in the configuration workbook.

Workshop	Participants	Decisions recorded
Organisation and access	Sponsor, System Administrator	Companies, branches, departments, reporting lines, users per role, two-step verification roles, security policy, <code>view:pii</code> per role
Sales, distribution and placement	Sales & Marketing, Processing Team	Lead assignment rules, channels, dealer programmes, placement journey per line, quotation validity, maker-checker, product templates, acceptance rules and authority, document templates
Policy servicing and renewals	Operations, Processing Team	Endorsements, cover notes, cancellation method (<code>pro-rata</code> , <code>short-period</code>), renewal timetable, fleets and open covers
Claims	Claims	Claims controls, document checklist, repair shops and letters of authority, settlement maker-checker
Billing, collection and remittance	Accounting, Accounting Manager	Billing mode per insurer, instalments, post-dated cheques, premium payment warranty, remittance terms and approval levels, bank payment

Workshop	Participants	Decisions recorded
		files
Commission and incentives	Accounting, Sales & Marketing	Commission rules, rate matrix, referrer withholding, payout conditions, insurer overrides
Ledger, close and tax	Accounting Manager, tax adviser	Chart of accounts, account determination, posting rules, payables, fixed assets, close checklist, tax codes and ATC, BIR forms, EOPT invoices, CAS books, EIS
Compliance	Compliance officer, DPO	AML/CFT risk factors, thresholds, monitoring rules, screening lists and provider; licence register; insurer authority check (warn or block); complaints deadlines; breach procedure
Integrations	IT head, Accounting, Operations	Banks and their file layouts, SMS or Viber provider, CTPL authentication provider and LTO feed, insurer APIs, payment gateway, EIS, AMLC reporting
Branding	Sponsor, marketing	Theme, logo, sign-in picture, document and e-mail branding, signatories and their e-signatures, brand pack, permission for any client marks

Output: the configuration workbook and the fit-gap register. Each register line is classed as Fit (delivered), Configure (setting or master data), Procedure (the broker changes how it works) or Gap (needs a change request).

5.5 Client inputs and the configuration kit

The broker fills the configuration kit with the consultants: company, settings, PSGC regions, provinces, cities and barangays, branches, departments, hierarchy, designations, users, currencies, exchange rates, chart of accounts, banks, bank accounts, signatories, transaction codes, write-off reasons, insurers, lines of business, products, policy types, covers, vehicles, suppliers, asset classes, short-period rates, cancellation reasons, claim document checklist, repair shops, commission rates, premium taxes, LGU rates, authority limits, numbering, payee bank accounts and COC series. User passwords are never in the workbook: each new user receives a temporary password once, after the load.

5.6 Regulatory registrations

Registration	Owner	What it unlocks
BIR Authority to Print or CAS registration; registered serial range; last numbers used	Accounting Manager with the tax adviser	Sales invoices (invoice.*), numbering, CAS books; release to Production
BIR EIS enrolment (when covered)	Accounting Manager	EIS connector live; until then it stays off
AMLC registration, portal access, institution code	Compliance officer	CTR and STR filing; go/no-go
IC licence data and insurer certificates of authority	Compliance officer	Licence register, payout check, insurer authority check
NPC registration of the DPO and data processing systems	DPO	Go/no-go
Screening lists (UN, AMLC; PEP list licence)	Compliance officer	Screening at onboarding, issue and payout; go/no-go

Registration	Owner	What it unlocks
Tax adviser confirmation of codes, ATC, rates and wording	Tax adviser	UAT sign-off

Lead times are assumptions; the Dependency Map and Critical Path gives them by size with their float.

5.7 Configuration

Configuration follows GO_LIVE_DATA_SETUP.md steps 1 to 12. The configuration kit is uploaded on Master > Go-Live and Data > Go-Live Data Load, validated as a trial run, corrected with the errors workbook and loaded, first in Dev (small, medium) or SIT (large, enterprise). The items without a sheet are set on their screens:

Item	Screen
Roles, permissions (including view:pii), segregation of duties, delegations, access reviews; approval of the loaded authority limits	Master > User Management
Product templates, rating factors, acceptance rules with refer, decline and loading and the authority to override, document templates with merge fields, market and risk mapping, the governing template of each product, the motor tariff	Product Configurator
Tax codes and ATC; account determination and posting rules (approved by a second user)	Master > Finance > Taxation, Account Determination, Posting Rules, Configuration Approvals
Statement formats, bank transaction types, insurer statement formats, close checklist, bank file layouts, payment gateways	Master > Finance
Settings, schedules, connectors, message templates, insurer mappings	Master > System Configuration
Fiscal years and periods (periods before the cutover date closed)	Accounts > Period End > Period Management
Remittance masters, reinsurance treaties, incentive programmes, referrer accounts, petty cash funds	Their screens

The delivered data already holds the PSGC addresses, ZIP codes, banks, ID types, holidays, the IC insurer list, Philippine lines of business and products, the motor tariff, the tax codes (VAT 12%, DST PHP 0.50 on each PHP 4.00 or fraction, LGT and expanded withholding codes with ATC) and a Philippine broker chart of accounts. Configuration therefore reviews and adjusts more than it builds. When frozen, configuration moves to UAT and Production as a **Current data** workbook of the source environment, and the comparison report shows the target mirrors the source.

5.8 Compliance set-up

- **AML/CFT:** AML Settings (covered transaction threshold, cash modes, CTR and STR working days, match threshold, risk score limits, KYC refresh months, beneficial owner threshold, retention, institution code), risk factors, monitoring rules, screening provider; the screening lists loaded and every client rescreened. The values delivered follow the AMLA and its rules as known at delivery: the compliance officer confirms them.

- **Insurance Commission:** licence register (firm, officers, licensed individuals, agents), fit and proper records, insurer certificates of authority; compliance.referrer_licence_check (block delivered) and compliance.insurer_authority_check (warn delivered, block once every certificate is entered); IC line mapping for the production report and account mapping for the annual statement.
- **Complaints:** channels, categories, deadlines (complaints.*), letter texts; confirmed against the IC rules in force.
- **Data privacy:** breach register owner and the 72-hour deadline settings, privacy notice version, masking of personal identifiers by role, consent rules for messages.

5.9 Branding and brand pack

The System Administrator brands UAT on Theme and Branding (theme, sign-in page, documents and reports, e-mail, name and images), captures the signatories' e-signatures with their consent and maps signatures to documents. The brand pack is exported and imported in Production with the configuration kit. A client brand pack that carries a third party's marks (for example the Toyota Insurance Services pack) is applied only in that client's environments and only with its written permission on file.

5.10 Data migration

The detail is in the Data Migration and Cutover Plan. In outline:

- The migration kit holds clients, in-force policies, open items, open claims and the GL opening balances as at the cutover date (golive.cutover_date). Migrated records keep their old numbers and post nothing; every validation shows a reconciliation of rows and totals.
- The broker extracts and cleanses the data; iorta TechNXT maps it with the broker, runs the loads with the broker and checks the reconciliation.
- Mock loads: small and medium, two in UAT; large, two in SIT and one in UAT; enterprise, two in SIT and two in UAT. Each runs on a fresh extract after a transaction reset. The cutover rehearsal in Pre-Prod is the last load before cutover for every size.

5.11 Integrations with partners

Every connector is delivered in test mode, so the process can be tested before the partner contract is signed. What is certified with each partner is done during onboarding with that partner.

Integration	Delivered	Implementation work	If the partner is late
E-mail	Outgoing mail through the broker's SMTP mailbox, queued in the E-mail Outbox; branded layout	Mailbox and credentials, sender, texts; password reset and approval link tested	Holds the go-live
Bank statements	Statement import with delivered formats; remittance bank transactions import	One statement per account imported with a balancing preview	Manual bank items
Bank	Starter layouts for BDO,	Each layout validated	Cheques and manual

Integration	Delivered	Implementation work	If the partner is late
payment files	BPI, Metrobank, Landbank, UnionBank and a generic CSV; status file import	against the bank's current specification and a test file accepted by the bank	transfers
SMS or Viber	Connectors SMS_SEMAPHORE, SMS_GLOBE_LABS, SMS_GENERIC, VIBER_BUSINESS; message templates with consent check	Provider account, sender name, credentials in the secret store, live test	E-mail notices; SMS jobs stay off
CTPL authentication and LTO	CTPL_AUTH and LTO_FEED connectors; COC series; authentication at issue	Accreditation with the IC-accredited provider, COC series loaded, one COC authenticated live	Enter code from the provider portal
Insurer systems	INSURER_API connector with a mapping per insurer; claim status file	Mapping, preview, test issuance and claim status with each insurer	Record Issued Policy; claim status file
Payment gateway	PayMongo and Dragonpay, and a sandbox provider	Merchant account, credentials, notification address; sandbox then live test payment	Bank transfer, cheque, cash
BIR EIS	EIS connector (off by default), test mode with a built-in fake provider	Test submissions; live after the BIR enrolment	Connector off; earlier invoices queued later
AMLC reporting	CTR and STR report files (BV-AMLC-TXN 1.0)	Portal access; test file checked against the portal requirements	Holds the go-live

5.12 Training

Train-the-trainer for the key users first, then end-user training per role, delivered by the key users with iorta TechNXT present. The compliance officer, the DPO and the System Administrator are trained by iorta TechNXT on the compliance and privacy screens. The Training Plan gives the curriculum and durations.

5.13 System integration test

iorta TechNXT runs the end-to-end flows across all roles with the configured masters: in Dev with synthetic data for a small or medium broker, in SIT with the migrated data of the latest mock load for a large or enterprise broker. The test follows the end-to-end plan (docs/e2e/E2E_TEST_PLAN.md), the scripted scenario backend/scripts/uat-scenario.js and the release test cases for the compliance, BIR and integration features, with every connector in test mode. Defects are logged with the request ID shown in error messages.

5.14 User acceptance test

Key users run docs/onboarding/UAT_SCRIPTS.md with the broker's own products, insurers and data, plus the scenarios agreed in discovery for the features the broker uses: client onboarding with screening and EDD, transaction alerts and a CTR file, licence and insurer authority checks, a complaint and a breach record, BIR forms and a sales invoice, bank payment files, CTPL authentication and the branded documents. Each scenario is marked Pass or Fail with date, name and, for a failure, the record number and request ID.

5.15 Rehearsal, cutover and go-live

- The release tag and the frozen configuration go to Production before the rehearsal; the production smoke test is followed by a transaction reset.
- Pre-Prod is restored from a production backup with its own secrets, e-mail off and the scheduler stopped; it is masked with `mask:data --remark-copy` first when people without production access take part.
- The rehearsal runs the transaction reset, the migration load of a fresh extract, the reconciliation, the go-live lock on and off, and the comparison against Production, each step timed.
- Cutover follows the Data Migration and Cutover Plan: freeze of the old system, final extract and load, reconciliation signed by Accounting and the Accounting Manager, go/no-go 2, then `golive.locked` and `npm run mask:data -- --register-production` in Production.

5.16 Hypercare

The project team stays with the broker after go-live: daily check-in in the first week, then weekly. Hypercare covers the first receipts, remittances, bank imports and payment files, the first month-end close and the first BIR and AMLC filings that fall in the window. It ends with the handover to production support. Default length: 2 weeks (small), 3 weeks (medium), 6 weeks (large and enterprise); if the first month-end close falls after that window, hypercare extends to cover it. Pre-Prod is removed after hypercare exit.

6. Timelines by size

6.1 Phases and milestones


Phase	Small	Medium	Large	Enterprise
Mobilisation	W1	W1	W1	W1
Environments and pipeline	W1 to W2	W1 to W3	W1 to W4	W1 to W5
Discovery and fit-gap	W1 to W2	W1 to W3	W1 to W4	W1 to W6
Client inputs	W1 to W2	W1 to W3	W1 to W4	W1 to W6
Regulatory registrations	W1 to W6	W1 to W6	W1 to W9	W1 to W12
Configuration (go-live configuration kit)	W2 to W4	W2 to W6	W3 to W10	W4 to W13
Compliance set-up	W3 to W4	W4 to W6	W6 to W8	W8 to W10
Branding and brand pack	W3 to W4	W4 to W5	W6 to W7	W8 to W9
Integrations with partners	W2 to W7	W2 to W10	W3 to W15	W3 to W21
Data migration (go-live migration kit)	W1 to W5	W1 to W7	W1 to W13	W1 to W18
Training	W4 to W6	W6 to W9	W8 to W14	W10 to W19
SIT and UAT	W4 to W6	W6 to W9	W10 to W14	W13 to W20
Rehearsal and cutover	W5 to W7	W8 to W10	W12 to W15	W16 to W21
Hypercare	W7 to W8	W10 to W12	W15 to W20	W21 to W26

Milestone	Small	Medium	Large	Enterprise
Kick-off	Start of W1	Start of W1	Start of W1	Start of W1
Configuration decisions and fit-gap signed	End of W2	End of W3	End of W4	End of W6
Configuration complete	End of W4	End of W6	End of W10	End of W13
SIT exit	End of W4	End of W7	End of W12	End of W16
UAT sign-off	End of W6	End of W9	End of W14	End of W20
Go/no-go	End of W6	End of W9	End of W14	End of W20
Go-live	Start of W7	Start of W10	Start of W15	Start of W21
Hypercare exit and handover	End of W8	End of W12	End of W20	End of W26

Integrations run to the go-live week because the EIS connector is switched on after the BIR enrolment; every other partner certification is planned before go-live.

6.2 Small broker (8 weeks)

Small broker: 8 weeks, go-live at the start of week 7

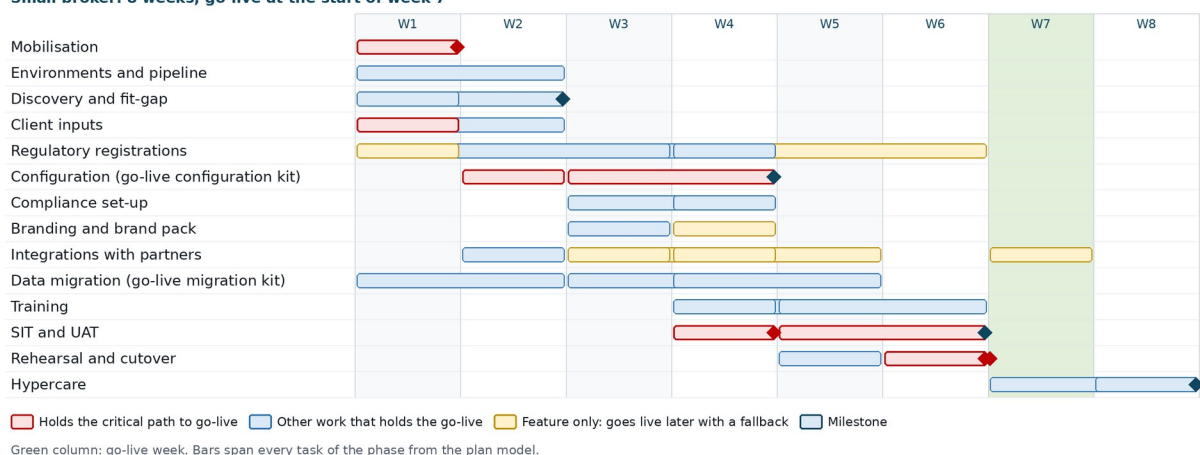


Small broker: phases by week. Red: tasks on the critical path to go-live

Week	Activities	Milestones
1	Kick-off; charter and RAID log; data request and kits issued; team named; hosting decided; Dev and UAT provisioned; GitHub Environments, secrets and keys; all workshops start; insurers, rates, products, chart of accounts and user list provided; registrations confirmed or started (ATP or CAS, EIS, AMLC, IC licences, NPC); extraction starts	Kick-off held
2	Workshops completed; configuration kit filled; first pipeline deployment; e-mail tested; Production provisioned; partner contracts and COC series; screening lists sourced	Fit-gap register signed
3	Configuration kit loaded in Dev; on-screen configuration; configuration promoted to UAT; mock load 1 in UAT starts; compliance set-up; branding and brand pack; bank statement imports; partner certifications start (bank files, SMS, CTPL, insurers, gateway)	
4	Mock load 1 reconciled; configuration completed; SIT in Dev; screening lists loaded; AMLC report file test; compliance officer and DPO training; tax adviser confirmation; EIS in test mode; ATP or CAS in place; train-the-trainer	Mock load 1 reconciled; configuration complete; SIT exit
5	Release candidate and frozen configuration to UAT; UAT starts; release to Production and smoke test; Pre-Prod from a production backup; mock load 2; end-user training; bank files and insurer APIs certified	Mock load 2 reconciled
6	UAT completed; end-user training completed; cutover rehearsal in Pre-Prod; go/no-go; cutover at the close of the week	UAT sign-off; go decision
7	Go-live; daily hypercare; first receipts, remittances and bank imports watched; EIS live once enrolled	Go-live
8	Hypercare; first month-end close where it falls; knowledge transfer; handover; Pre-	Hypercare exit and handover

Week	Activities	Milestones
	Prod removed	

6.3 Medium broker (12 weeks)

Medium broker: 12 weeks, go-live at the start of week 10

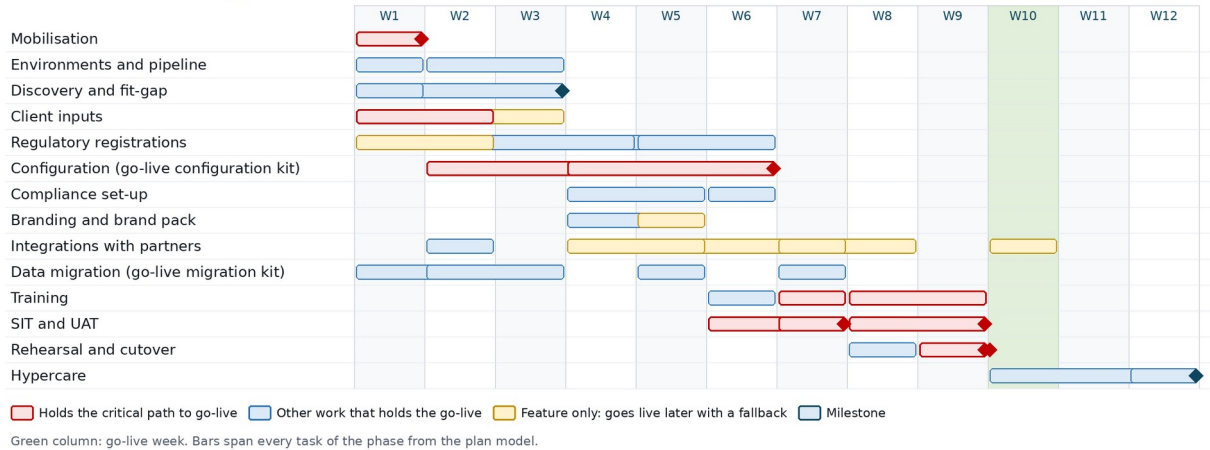


Medium broker: phases by week

Week	Activities	Milestones
1	Kick-off; governance; data request and kits; team named; hosting decided; Dev and UAT provisioned; workshops start; registrations confirmed or started; extraction starts	Kick-off held
2	GitHub Environments, secrets and keys; first pipeline deployment; e-mail tested; insurers, rates, products and chart of accounts provided; configuration kit filling starts; Production provisioned	
3	Workshops completed; mapping to the migration kit; partner contracts	Fit-gap register signed
4	Configuration kit loaded in Dev; on-screen configuration starts; configuration promoted to UAT; compliance set-up; branding; partner certifications start	
5	Mock load 1 in UAT; bank statement imports; payment gateway; ATP or CAS in place	Mock load 1 reconciled
6	Configuration completed; SIT cycle 1; screening lists loaded; AMLC report file test; compliance officer and DPO training; tax adviser confirmation	Configuration complete
7	SIT cycle 2 and exit; promotion to UAT; mock load 2; train-the-trainer; EIS in test mode; bank payment files certified	SIT exit; mock load 2 reconciled
8	UAT cycle 1; end-user training; release to Production; Pre-Prod; insurer APIs certified	UAT cycle 1 results
9	UAT cycle 2; end-user training completed; cutover rehearsal in Pre-Prod; go/no-go; cutover	UAT sign-off; go decision
10	Go-live; daily hypercare; EIS live once enrolled	Go-live
11	Hypercare; first remittance run and bank reconciliations	Weekly hypercare review
12	Hypercare; first month-end close supported; knowledge transfer; handover; Pre-Prod removed	Hypercare exit and handover

6.4 Large broker (20 weeks)

Large broker: 20 weeks, go-live at the start of week 15

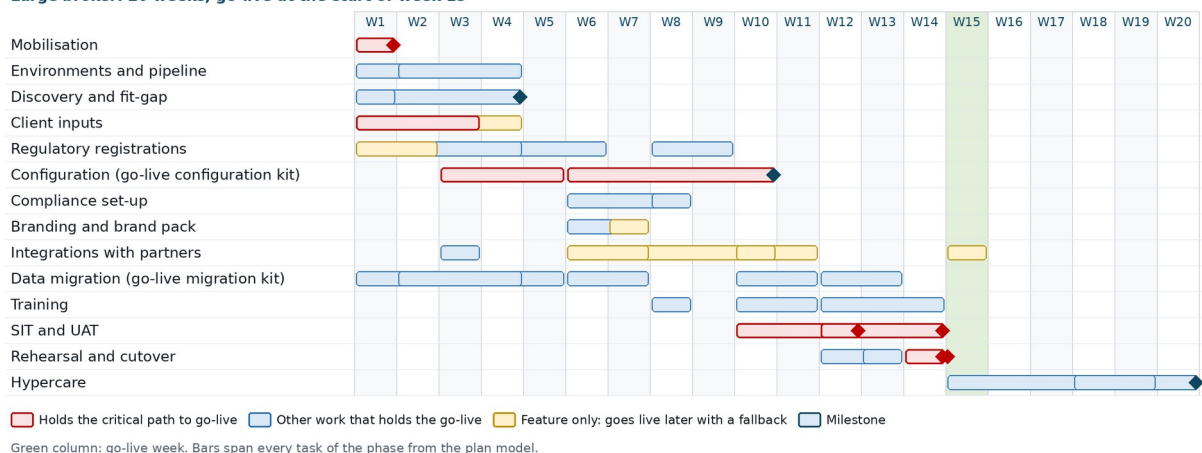

Large broker: phases by week


Week	Activities	Milestones
1	Kick-off; governance; data request and kits; team named; hosting decided; workshops start; registrations confirmed or started; extraction starts	Kick-off held
2	Dev, SIT and UAT provisioned; GitHub Environments, secrets and keys; Production provisioning starts; partner contracts	
3	First pipeline deployment to Dev, SIT and UAT; e-mail tested; insurers, rates, products and chart of accounts provided; configuration kit filling starts	Environments ready
4	Workshops completed; mapping	Fit-gap register signed
5	Configuration kit filled	
6	Configuration kit loaded in SIT; on-screen configuration; compliance set-up; branding; bank statement imports; mock load 1 in SIT; partner certifications start	
7	Mock load 1 reconciled; branding and brand pack completed	Mock load 1 reconciled
8	Compliance set-up completed; screening lists loaded; AMLC report file test; compliance officer and DPO training; tax adviser review	
9	Configuration continues; CTPL authentication certified	
10	Configuration completed; SIT starts; mock load 2 in SIT; train-the-trainer; EIS in test mode; bank payment files certified	Configuration complete
11	SIT; mock load 2 reconciled; insurer APIs certified	Mock load 2 reconciled
12	SIT exit; promotion to UAT; UAT starts; mock load 3 in UAT; end-user training (head office); release to Production	SIT exit
13	UAT; Pre-Prod from a production backup; end-user training (branches)	Mock load 3 reconciled
14	UAT completed; cutover rehearsal in Pre-Prod; go/no-go; cutover	UAT sign-off; go decision
15	Go-live for all branches; daily hypercare at head office; floor walkers in the branches	Go-live
16 to 17	Hypercare; first remittance runs, bank reconciliations, payment files, collection, commission payout and renewal cycles	Weekly hypercare review
18 to 19	First month-end close and BIR working papers of the first month (timing depends on the go-live date); settings review	First close completed

Week	Activities	Milestones
20	Knowledge transfer; handover; Pre-Prod removed	Hypercare exit and handover

All branches go live on one date, because the ledger, the receivables and the amounts due to insurers move to BrokerVerse at a single cutover. A large broker with one office cluster and a simple product mix can follow a 16-week variant: discovery ends in week 4, configuration in week 8, three mock loads (the last as the rehearsal in Pre-Prod), go-live at the start of week 13 and hypercare in weeks 13 to 16 (extended to the first month-end close if needed).

6.5 Enterprise broker (26 weeks)

Enterprise broker: 26 weeks, go-live at the start of week 21

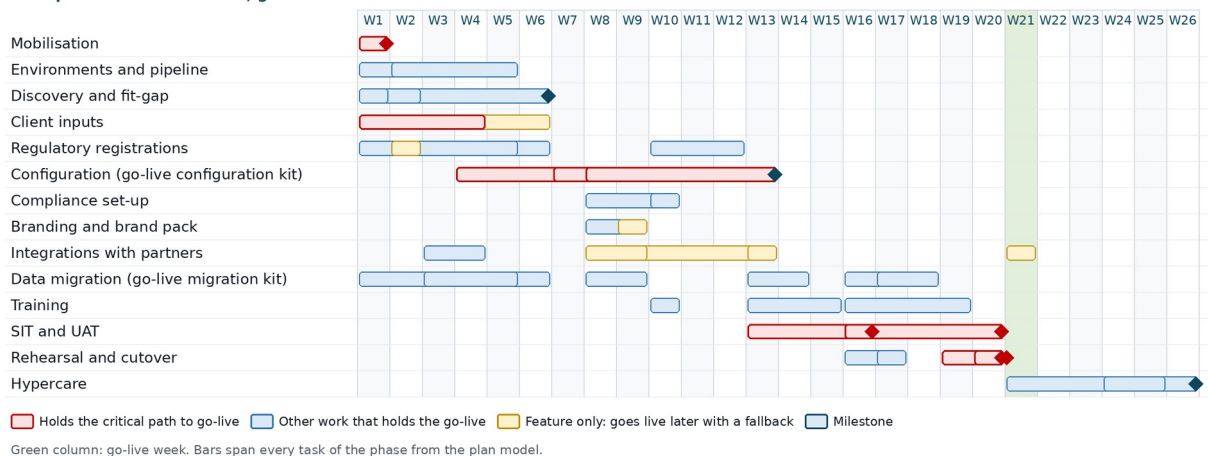

Enterprise broker: phases by week

Week	Activities	Milestones
1 to 2	Kick-off; governance; data request and kits; team named; hosting decided; Dev, SIT and UAT provisioned; GitHub Environments, secrets and keys; workshops start; registrations confirmed or started; extraction starts	Kick-off held
3 to 5	First pipeline deployment; e-mail tested; Production provisioned (high availability, cross-region backup copy); insurers, rates, products and chart of accounts provided; configuration kit filling starts; mapping	Environments ready
6	Workshops completed; partner contracts completed	Fit-gap register signed
7 to 8	Configuration kit filled and loaded in SIT; on-screen configuration starts; compliance set-up; branding; mock load 1 in SIT starts; partner certifications start	
9 to 12	Mock load 1 reconciled; on-screen configuration; screening lists loaded; AMLC report file test; compliance officer and DPO training; CTPL authentication certified; tax adviser confirmation	Mock load 1 reconciled
13	Configuration completed; SIT starts; mock load 2 in SIT; train-the-trainer starts; EIS in test mode; bank payment files and insurer APIs certified	Configuration complete
14 to 15	SIT; mock load 2 reconciled; train-the-trainer completed	Mock load 2 reconciled
16	SIT exit; promotion to UAT; UAT starts; mock load 3 in UAT; end-user training starts; release to Production	SIT exit
17 to 18	UAT; Pre-Prod; mock load 4 in UAT	Mock loads 3 and 4 reconciled

Week	Activities	Milestones
19 to 20	UAT completed; end-user training completed; cutover rehearsal in Pre-Prod; go/no-go; cutover	UAT sign-off; go decision
21	Go-live for every branch and channel; daily hypercare; EIS live once enrolled	Go-live
22 to 23	Hypercare; remittance, bank, payment file, commission and renewal cycles	Weekly hypercare review
24 to 25	First month-end close and the first BIR and AMLC filings	First close completed
26	Knowledge transfer; handover; Pre-Prod removed	Hypercare exit and handover

The enterprise plan is the reference; the actual plan is set at mobilisation with the number of lines of business, insurers, branches and channels.

6.6 Task-level plan

The workbook holds the task-level plan of each size: 77 tasks in 14 phases (fewer for small and medium, which have no SIT environment and fewer mock loads), each with its duration in working days, owner party, owner role, deliverable or evidence, predecessors, start and finish dates from the kick-off date typed on the sheet, float to go-live and whether it is on the critical path. The table below lists the tasks, their owner and what each holds back.

ID	Task	Party	Owner role	Holds back
M1 to M5	Kick-off; charter, plan, governance, RAID log; data request and kits; broker team named; hosting and environment set	iorta TechNXT; broker	iorta TechNXT PM; broker sponsor	Go-live
E1 to E7	Dev, SIT, UAT provisioned; GitHub Environments; secrets and keys with custody; first pipeline deployment; Production with backups and restore test	iorta TechNXT	DevOps lead	Go-live
D1 to D5	Process, compliance, integration and branding workshops; fit-gap signed	iorta TechNXT; broker	Consultants; process owners	Go-live
I1 to I10	Insurers and rates; chart of accounts; user list; SMTP; banks; partner contracts; COC series; images and signatories; training rooms; UAT testers	Broker	Key users, Accounting Manager, System Administrator, IT head, PM	Go-live, except partner contracts and COC series (feature only)
R1 to R8	ATP or CAS; EIS enrolment; AMLC registration; IC licence data; NPC registration; tax adviser confirmation; screening lists; permission for client marks	Broker	Accounting Manager, compliance officer, DPO, tax adviser, sponsor	Go-live, except EIS and client marks (feature only)
C1 to C5	Configuration kit filled and loaded; on-screen configuration; promotion to UAT for mock 1; configuration complete	Broker; iorta TechNXT	Key users; consultants	Go-live (critical path)
K1 to K3	Compliance set-up; screening lists loaded; AMLC report file test	iorta TechNXT; broker	Consultant; compliance officer	Go-live
B1, B2	Branding, e-signatures and brand pack; client brand pack with	iorta TechNXT	Consultant	Go-live; client pack feature only

ID	Task	Party	Owner role	Holds back
	permission			
N1 to N9	E-mail; bank statements; bank payment files; SMS; CTPL and LTO; insurer APIs; payment gateway; EIS test and live	iorta TechNXT; partner	DevOps lead, consultants; banks, providers, insurers	E-mail and statements: go-live; the others feature only
G1 to G6	Extraction and cleansing; mapping; mock loads 1 to 4	Broker; iorta TechNXT	Data owners; migration lead	Go-live
L1 to L3	Train-the-trainer; compliance officer and DPO training; end-user training	iorta TechNXT; broker	Consultants; key users	Go-live
T1 to T5	SIT; SIT exit; promotion to UAT; UAT; UAT sign-off	iorta TechNXT; broker	Test lead; key users; sponsor	Go-live (critical path)
X1 to X6	Release to Production; Pre-Prod; rehearsal; go/no-go 1; cutover; go-live	iorta TechNXT; broker	DevOps lead, migration lead; steering committee	Go-live (critical path)
H1 to H3	Hypercare; first month-end close; handover	iorta TechNXT; broker	PM; Accounting Manager; support manager	Hypercare exit

The critical path is the same for every size: client data for the configuration kit, configuration, SIT, UAT, rehearsal, go/no-go, cutover. The Dependency Map and Critical Path shows it per size with the near-critical tasks and the effect of each late dependency.

7. Roles and responsibilities

7.1 Project roles

Role	Party	Responsibilities
Project sponsor	Broker	Chairs the steering committee; approves scope, change requests, go/no-go; permission for any client marks
Project manager	Broker	Plans the broker's work, obtains data, decisions and registrations, runs UAT and training logistics
Process owners and key users	Broker	One per team; take part in discovery, fill the configuration kit, test, train their team
System Administrator	Broker	Users, roles, masters, settings, branding and loads after go-live; second line of support
Accounting Manager	Broker	Chart of accounts, posting rules, tax set-up, ATP or CAS, EIS enrolment, opening balances, close; signs off the financial reconciliation
Compliance officer	Broker	AML/CFT programme and settings, screening lists, AMLC registration and filings, IC licences, complaints
Data protection officer	Broker	NPC registration, privacy notice, masking approvals, breach register, privacy impact assessment
IT head	Broker	Hosting decision, partner credentials in the secret store, key custody with iorta TechNXT, network and devices
Tax adviser	Broker	Confirms tax codes, ATC, rates, invoice and receipt wording
Partners	Banks, SMS provider, CTPL authentication provider, insurers, payment gateway	Certify their interface with the broker
Head of delivery	iorta TechNXT	Delivery quality and resources; steering committee member when cost or the go-live date is at stake
Project manager	iorta TechNXT	Plan, RAID log, dependencies, status reports, steering committee papers
Functional consultants	iorta TechNXT	Discovery, configuration, compliance set-up, branding, SIT, training of key users, UAT support
Migration lead	iorta TechNXT	Mapping, mock loads, reconciliation, rehearsal, cutover loads
Technical and DevOps lead	iorta TechNXT	Environments, pipeline, GitHub Environments, secrets and keys, connectors, backups, monitoring, Pre-Prod, cutover execution

7.2 RACI

R = Responsible, A = Accountable, C = Consulted, I = Informed. The full matrix, with the broker compliance officer and DPO and the partners as separate columns, is in the workbook.

Activity	iorta TechNXT PM	iorta TechNXT team	Broker sponsor and PM	Broker key users, IT, compliance
Project plan and governance	R	Consultants C Technical C	Sponsor A PM R	Key users I IT I
Data request, kits and extraction	C	Consultants C	PM A	Key users R IT R
Discovery workshops	A	Consultants R	PM R	Key users R Compliance C
Configuration decisions	C	Consultants R	PM A	Key users R IT C
Configuration kit and on-screen configuration	A	Consultants R Technical C	PM C	Key users R IT R
Environments, pipeline, backups, monitoring	A	Technical R	PM I	IT C
Encryption keys and their custody	I	Technical R	PM I	IT A
Regulatory registrations	I	Consultants C	Sponsor A PM R	Accounting Manager R Compliance R
Compliance set-up	I	Consultants R	PM C	Compliance A
Branding, e-signatures, brand pack	A	Consultants R	Sponsor C PM C	IT R
Mock loads and reconciliation	A	Consultants R Technical R	PM C	Key users R Accounting Manager R
Partner integrations	C	Consultants R Technical R	PM A	IT R Partners R
System integration test	A	Consultants R Technical R	PM I	Key users C
UAT execution and sign-off	C	Consultants C	Sponsor A PM R	Key users R Compliance R
Training	A (TTT)	Consultants R	PM A (end users)	Key users R
Cutover execution	A	Consultants R Technical R	PM R	Key users R IT R
Go/no-go decision	C	Consultants C Technical C	Sponsor A PM R	Key users C Compliance C
Hypercare and handover	A	Consultants R Technical R	PM R	IT R

8. Governance

8.1 Steering committee

Item	Detail
Members	Broker sponsor (chair), broker project manager, Accounting Manager, compliance officer, a business head; iorta TechNXT account manager and project manager, with the head of delivery when cost or the go-live date is at stake
Frequency	Every two weeks, plus a meeting for each go/no-go
Inputs	Status report, milestone tracker, RAID log extract, dependencies due and late, change requests for decision
Decisions	Scope, change requests, plan changes, phase acceptance, go/no-go, hypercare exit

8.2 Weekly status

A weekly meeting of both project managers and the leads, with a written status report: progress against the plan, milestones due and done, decisions needed, top risks and issues, dependencies due in the next two weeks (data, registrations, partner certifications), next week's activities. Status uses green, amber and red against the baselined plan.

8.3 RAID log

One shared log of risks, assumptions, issues and dependencies, kept by the iorta TechNXT project manager and reviewed in every weekly status meeting. The template is pre-filled with the risks, assumptions and dependencies typical of an implementation, including partner certification, list licences for screening, tax adviser confirmations, regulatory registrations, key custody and data quality of the migration.

Field	Content
ID, type	R, A, I or D with a running number
Description	What it is and its effect on scope, time or quality
Owner	One named person
Rating	Probability and impact for risks (score and High, Medium, Low); impact for issues
Action and due date	Mitigation or resolution and when
Status	Open, in progress, closed; closure date

High items go to the steering committee. A dependency on the critical path late by 3 working days, or any dependency late by more than its float, is escalated with its effect on the go-live.

9. Deliverables and acceptance criteria

Phase	Deliverables	Acceptance criteria
Mobilisation	Project charter, baselined plan workbook, RAID log, data request list, blank kits, governance calendar	Charter and plan signed by both project managers and the sponsor
Environments and pipeline	Environment set of the size, environment sheet (addresses, backups, monitoring, GitHub Environments), key custody record	Smoke test passed on each; restore test done once; key custody record signed
Discovery and fit-gap	Configuration workbook, fit-gap register	Every process walked through; every register line classed and owned; signed by the process owners
Configuration	Configuration kit loaded in Dev or SIT and promoted to UAT; configuration workbook updated	Batches Loaded without errors; each item of GO_LIVE_DATA_SETUP.md set; test quotation premiums and taxes agree with manual calculations; comparison report shows UAT mirrors the source
Compliance set-up	AML settings, risk factors, rules, screening lists; licence register, fit and proper, insurer authority; complaints and breach settings; role masking	Compliance officer and DPO confirm the settings in writing; every client screened; CTR test file generated
Branding	Theme, documents, e-mails, e-signatures, brand pack	Sample documents and e-mails approved by the sponsor; permission on file for any client marks
Data migration	Mapping sheets, filled migration kits, load history, reconciliation workbooks of each mock load	Counts and totals agree within the agreed tolerance (default: exact); trial balance as at the cutover date agrees with the old system
Integrations	E-mail, bank statement formats, and each partner integration in scope	Password reset e-mail received; one statement per account imported; for each partner in scope, the certification of the Dependency Map passed or its fallback agreed at go/no-go
Training	Training schedule, attendance lists, assessment results	Every user trained in the role before go-live; key users pass at 90%
SIT	SIT plan, results, defect log, SIT exit report	All end-to-end flows passed; no open severity 1 or 2 defect
UAT	UAT results per script, defect log, UAT Sign-off Certificate	All scripts passed or accepted with a workaround; sign-off by each process owner and the sponsor
Rehearsal and cutover	Rehearsal log with timings, cutover checklist, final reconciliation, go/no-go minutes	Go/no-go criteria of the Data Migration and Cutover Plan met; registrations of the Dependency Map in place
Go-live	Production in use; go-live communication	Users signed in and transacting; first receipts, remittances and bank imports processed
Hypercare	Hypercare log, first month-end close support, configuration baseline, handover pack	No open severity 1 or 2 issue; first close completed; handover accepted by production support and the System Administrator

A deliverable is deemed accepted when the broker has not raised a written objection within 5 business days of submission, as the Statement of Work provides.

10. Assumptions

- The implementation is OOTB: the broker uses the delivered screens, workflows, reports and printed documents.
- The broker names a project manager and one key user per team, available at least 50% of their time during discovery, UAT and cutover, an Accounting Manager, a compliance officer and a DPO.
- The broker provides complete and cleansed data in the delivered kits by the dates in the plan.
- Decisions in discovery are made within 3 business days of each workshop.
- The broker holds, or obtains in the lead times of the Dependency Map, its BIR ATP or CAS registration, its AMLC registration, its NPC registration and the IC licences of the firm, officers and agents.
- The broker contracts its partners (banks for payment files, SMS provider, CTPL authentication provider, insurers for APIs, payment gateway) and obtains the screening lists and any PEP list licence.
- iorta TechNXT hosts the environment set of the size and the temporary Pre-Prod on AWS (region ap-southeast-1), priced per environment. Other hosting is priced separately and provides the same set.
- Workshops and training are delivered on site in Metro Manila or online, in English, during Philippine business hours.
- One legal entity and one fiscal year are migrated; opening balances are taken at a single cutover date.
- The broker uses the delivered roles: System Administrator, Sales & Marketing, Processing Team, Operations, Claims, Accounting, Accounting Manager and Compliance Officer (AML/CFT).
- The delivered tax codes, rates, BIR forms and AML values are confirmed by the broker's tax adviser and compliance officer before go-live.

11. Exclusions

The following are outside the OOTB implementation. Any of them can be quoted separately through a change request.

- Customisation of screens, workflows, reports, printed documents or the database, and new reports beyond the Report Builder.
- Connectors other than those delivered (SMS, Viber, CTPL authentication, LTO feed, insurer API, bank files, payment gateways PayMongo and Dragonpay, BIR EIS), for example core banking, accounting packages, BIR eFPS or eBIRForms filing, or an IC system.
- The partner's own work and fees: bank file certification fees, SMS and gateway fees, CTPL authentication fees, insurer API access.
- Data cleansing, de-duplication and enrichment of the broker's data, and extraction from the old system.
- Migration of closed or expired policies, settled claims, paid receivables, transaction history and documents, and more than one fiscal year of balances.
- Screening list content and PEP list licences; no list content is delivered with BrokerVerse.
- Hardware, end-user devices, networks, browsers and office software.
- Regulatory filings and registrations: BIR returns, alphalists and DAT files, CAS registration, ATP, EIS enrolment, IC reports and licences, NPC registration and breach notifications, AMLC registration and reports. The system prepares them; filing remains with the broker.
- Tax, legal, actuarial, AML or audit advice.
- Translation of the screens.
- Training beyond the curriculum of the Training Plan and training of users added after go-live.
- Support after hypercare, which is covered by the production support agreement.

12. Dependencies on the broker

Dependency	Needed by (Small / Medium / Large / Enterprise)
Named project manager, key users, Accounting Manager, System Administrator, compliance officer and DPO	W1 for every size
Hosting option, environment set and data location decision	W1
Insurer list and agreements, commission and referrer rates, product list; chart of accounts and mapping	W1 / W2 / W3 / W4 (critical path)
User list with roles, branches and reporting lines	W1 / W2 / W3 / W3
SMTP mailbox; bank accounts, statement samples, payee accounts	W1 to W2 / W2 / W2 to W3 / W2 to W3
Partner contracts and credentials; COC series	W2 / W3 / W4 / W6
BIR ATP or CAS and the invoice serial range; last numbers used	W4 / W5 / W6 / W6
AMLC registration and portal access; screening lists and PEP licence	W3 / W4 / W4 / W5
IC licence data and insurer certificates; NPC registration	W2 to W4 / W2 to W5 / W3 to W6 / W3 to W6
Tax adviser confirmation	W4 / W6 / W9 / W12
Migration extracts in the kit	Before each mock load and at cutover
Training rooms, devices and attendance; UAT testers and sign-off authority	Before training and UAT
Freeze of the old system and final extract	Cutover
Decisions on the fit-gap register and change requests	Within 3 business days

The Dependency Map and Critical Path gives the float of each dependency and what moves when it is late.

13. Risks and mitigations

The RAID log template is pre-filled with these risks and with their scoring; the list below is the summary.

Risk	Effect	Mitigation
Insurer, product, commission or chart of accounts data late	Configuration and every later phase slip day for day	Data requests in week 1; kits handed out at kick-off; data readiness tracked weekly; escalation after 3 days
Poor data quality in the old system	Rejected rows; balances do not reconcile	Mock loads on fresh extracts; errors workbook; the broker cleanses at source
Partner certification late (bank files, CTPL authentication, insurer APIs, SMS, gateway)	Feature not live at go-live	Contracts in week 1 to 2; connectors in test mode; fallbacks agreed at go/no-go
Registration late (ATP or CAS, AMLC, NPC)	Go-live moves; invoices or filings not possible	Confirm or start on the kick-off day; tracked as dependencies with the broker owner
Screening list licence not obtained	Screening incomplete at go-live	UN and AMLC lists loaded first; PEP list licence started after the compliance workshop
Tax adviser confirmation late	VAT, withholding or invoice wording wrong	Review booked in the configuration phase; UAT sign-off depends on it
Encryption key lost or not escrowed	Backups unreadable; personal identifiers lost	Key custody record before Production is provisioned; key kept with the backups; rotation procedure
Client marks used without permission	Trademark exposure	Client brand pack applied only with written permission on file
Requests for customisation	Scope and timeline grow	Configure-first; fit-gap classes; change request process
Key users unavailable	Decisions late; weak UAT and training	Named key users with committed time; backups named
Opening balances and open items do not agree	Ledger wrong from day one	Reconciliation in every load; Accounting Manager signs off
First month-end close outside hypercare	Close issues found late	Hypercare extends to the first close

14. Change request process

A change request covers any change to the agreed scope, plan or deliverables, including any gap from the fit-gap register.

1. The requester writes the change request: description, reason, business impact, priority.
2. The iorta TechNXT project manager logs it and, within 5 business days, returns an impact assessment: effort, cost, effect on the timeline and on other deliverables, and whether it can be met by configuration instead.
3. The broker project manager reviews the assessment with the process owner.
4. The steering committee approves, rejects or defers it. Changes that affect cost or the go-live date need the sponsor's written approval.
5. An approved change request is added to the plan and the RAID log and is tracked to closure.
6. A rejected or deferred change request stays in the log with the reason.

Customisation approved through a change request is built, tested and released under the release process of the Production Support Approach and Standards, and may be scheduled after go-live so the OOTB go-live date holds.

15. Document Sign-Off

Serial Number	Description	Owner	Status
1	No open items at the time of issue	iorta TechNXT	

Sign Off Date	Signature	Approved By	Department & Project Role



Insurance technology for the Philippines



10+

COUNTRIES

Global Presence



8

GLOBAL OFFICES

Strategically Located



11+

MARKETS SERVED

Across Continents



100%

COMMITMENT

To Excellence



MALAYSIA



INDIA



PHILIPPINES



THAILAND



VIETNAM



USA



ETHIOPIA



CAMBODIA



HONGKONG



SINGAPORE



Scan More Details
