



Dependency Map and Critical Path

BrokerVerse OOTB

Prepared by – **iorta TechNXT**

Version – **1.0**

Date – **04 October 2026**

TABLE OF CONTENTS

1. Document Control.....	3
2. Acronyms.....	3
3. Introduction.....	4
3.1 Purpose.....	4
3.2 How the figures are produced.....	4
3.3 Terms.....	5
3.4 Version history.....	5
3.5 Related documents.....	5
4. The dependency map.....	6
4.1 Phases and gates.....	6
4.2 Three kinds of gate.....	7
5. Client inputs.....	8
5.1 What the broker provides.....	8
5.2 The kits the inputs go into.....	9
6. Partner certifications.....	10
6.1 Partners and fallbacks.....	10
6.2 When each partner must be live.....	11
7. Regulatory registrations.....	13
7.1 What the broker registers, and what it unlocks.....	13
8. Environments, pipeline and keys.....	15
8.1 Set-up order.....	15
8.2 Encryption key custody.....	17
9. Critical path by size.....	19
9.1 How to read the charts.....	19
9.2 Small broker (8 weeks).....	19
9.3 Medium broker (12 weeks).....	20
9.4 Large broker (20 weeks).....	20
9.5 Enterprise broker (26 weeks).....	21
10. Lead times.....	22
11. What slips if a dependency slips.....	23
11.1 Dependencies that hold the go-live.....	23
11.2 What else moves with it.....	24
11.3 Feature-only dependencies.....	24
12. Managing the dependencies.....	26
13. Document Sign-Off.....	27

1. Document Control

Date	Version	Author & Business Unit Info	Reviewed By & Business Unit Info	Approved By & Business Unit Info	Change History
04 October 2026	1.0	iorta TechNXT			Initial issue: dependencies, lead times, critical path by size and the effect of each late dependency

2. Acronyms

Acronym / Symbol	Definition / Meaning
OOTB	Out of the box
AMLC	Anti-Money Laundering Council
ATP	Authority to Print
BIR	Bureau of Internal Revenue
CAS	Computerized Accounting System
COC	Certificate of cover
CTPL	Compulsory Third Party Liability
CTR	Covered transaction report
DPO	Data protection officer
EIS	Electronic Invoicing System
GNG	Go/no-go
IC	Insurance Commission
LTO	Land Transportation Office
NPC	National Privacy Commission
PEP	Politically exposed person
PM	Project manager
RAID	Risks, assumptions, issues and dependencies

SIT	System integration test
STR	Suspicious transaction report
UAT	User acceptance test

3. Introduction

3.1 Purpose

This document shows what a BrokerVerse OOTB implementation depends on, in what order, and what moves when a dependency is late. It is written for the iorta TechNXT head of delivery and project managers, and for the broker's sponsor and project manager. It answers four questions:

1. Which client inputs, partner certifications, regulatory registrations and environment steps does each phase need?
2. Which chain of tasks decides the go-live date for a small, medium, large and enterprise broker?
3. How long does each outside party usually take (lead time), and by when must it start?
4. If a dependency slips, does the go-live move, or only one feature, and by how much?

3.2 How the figures are produced

Every figure in this document comes from one plan model kept with the documentation tools (docs/package/tools/delivery/plan_model.py). The model holds each task with its duration by size, its owner party (iorta TechNXT, broker or partner), its predecessors and what it holds back. A forward and backward pass over the links gives the dates, the float of each task and the critical path. The same model builds the companion workbook BrokerVerse_Implementation_Plan.xlsx (one task-level Gantt per size, the milestones, every link and the RACI) and the diagrams of this document, so the three never disagree.

Durations and lead times are planning assumptions of iorta TechNXT for an out-of-the-box implementation. Lead times of regulators and partners are outside the control of both parties. The steering committee re-baselines the plan at mobilisation, once the broker has said which registrations it already holds and which partners it uses.

3.3 Terms

Term	Meaning
Day, week	Working days (5 a week). Week 1 starts on the kick-off date. Go-live is the first day of the go-live week
Float to go-live	Working days a task can finish late before the go-live date moves. 0 means the task is on the critical path
Holds the go-live	The go/no-go cannot pass while the dependency is open
Feature only	The go-live does not wait; the feature is switched on later and a fallback, described in this document, is used meanwhile
Lead time	Elapsed time an outside party needs from a complete request to the result

3.4 Version history


Version	Date	Change
1.0	04 October 2026	Initial issue: dependency diagrams, client inputs, partner certifications, regulatory registrations, environments and keys, critical path by size, lead times, effect of a late dependency

3.5 Related documents

Document	Use
BrokerVerse Implementation Approach and Plan	Method, phases, timelines by size, roles, governance
BrokerVerse_Implementation_Plan.xlsx	Task-level plan by size: durations, owners, predecessors, dates, float, critical path; RACI
BrokerVerse_RAID_Log_Template.xlsx	Pre-filled risks, assumptions, issues and dependencies; the dependencies of this document are its D items
BrokerVerse Environment Strategy and Production Rollout	Environment sets, pipeline, cutover runbook T-30 to T+30
BrokerVerse Data Migration and Cutover Plan	Mock loads, reconciliation, go/no-go criteria
Implementation Statement of Work; Customer Responsibilities and RACI Annex	The contractual form of the client dependencies and their effect when late

4. The dependency map

4.1 Phases and gates

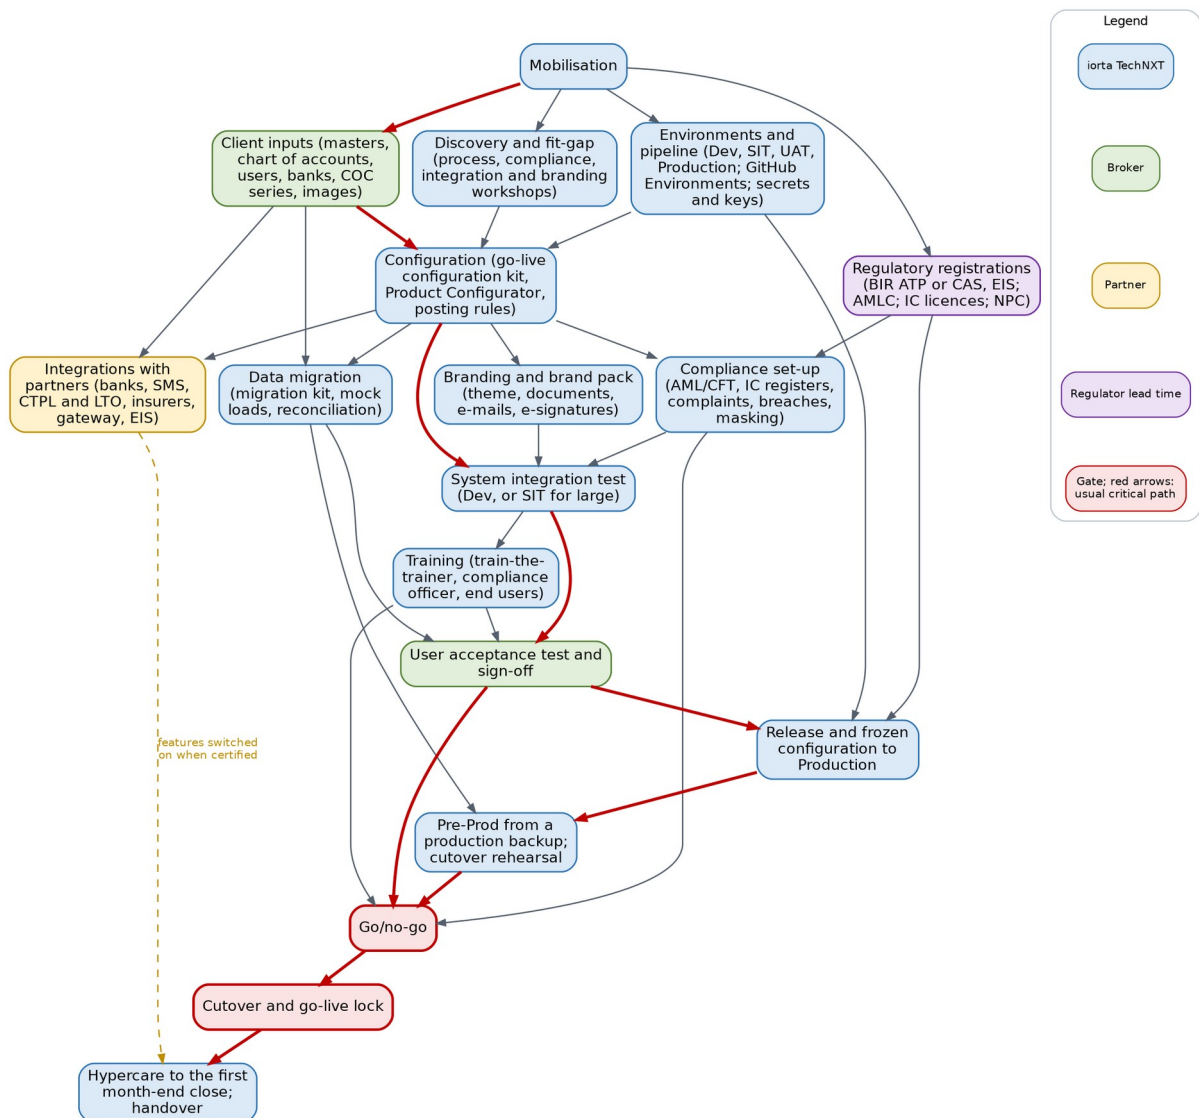

Dependency map of the phases. Red arrows: the usual critical path; dashed: features switched on when the partner has certified them

Reading the map:

- **Mobilisation** releases four streams in week 1: the client inputs (the configuration kit and the data request), discovery, the environments and the regulatory registrations. Registrations with a regulator start on day one because their lead times are the longest and are not in the project's hands.
- **Configuration** needs all three of discovery decisions, client inputs and a working Dev (or SIT) environment with the pipeline. It is the hinge of the plan: compliance set-up, branding, integrations and the mock loads all start from a loaded configuration kit.


- **System integration test** needs configuration, compliance set-up and branding finished. UAT needs SIT exit, trained key users and a reconciled mock load.
- **Release to Production** needs UAT under way, the production environment and the BIR invoice registration (ATP or CAS), because the invoice serial range is part of the frozen configuration.
- **Go/no-go** brings everything together: UAT sign-off, the reconciled rehearsal, trained users, compliance set-up (screening lists, AMLC reporting) and the NPC registration.
- **Integrations with partners** mostly do not hold the go-live: each has a fallback, and the feature is switched on when the partner has certified it (chapter Partner certifications).

4.2 Three kinds of gate

Gate	What happens when the dependency is late	Examples
Holds the go-live	The go/no-go fails; the go-live date moves by the delay less the float	Configuration kit inputs, UAT, rehearsal, ATP or CAS, AMLC registration, screening lists, NPC registration
Feature only	The go-live holds; the feature stays in test mode or switched off and the fallback is used	Bank payment files, SMS, insurer APIs, payment gateway, EIS, CTPL authentication (manual code entry), client brand pack
Hypercare exit	Hypercare is extended	First month-end close outside the hypercare window

5. Client inputs

5.1 What the broker provides

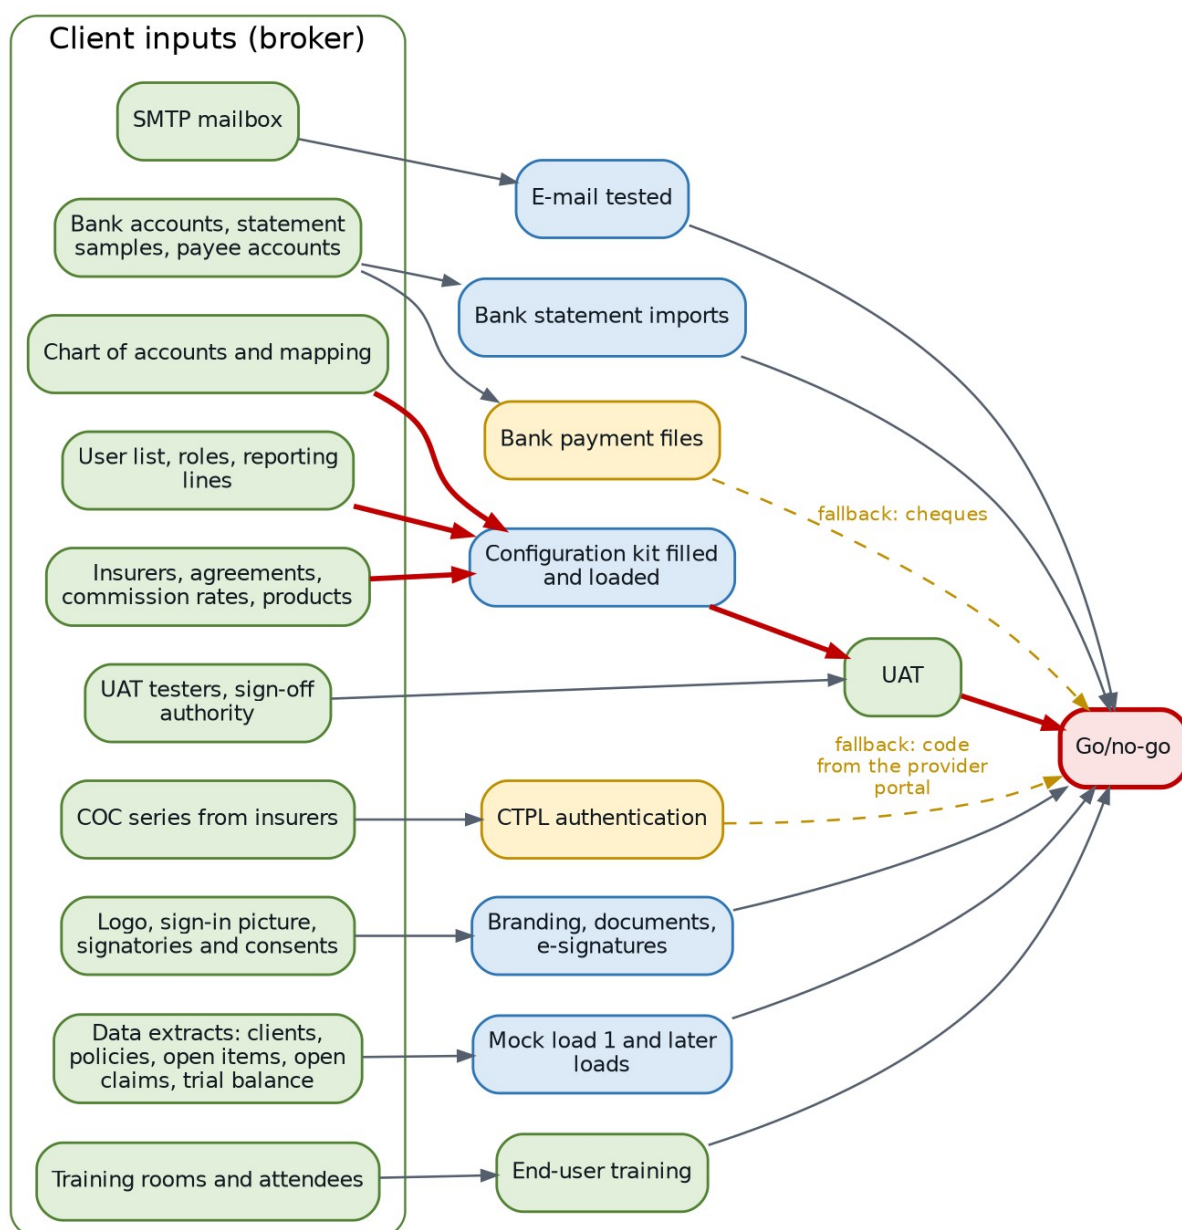

Client inputs and what each feeds. Red: on the critical path for every size

ID	Input	Owner (broker)	Needed by: Small / Medium / Large / Enterprise	Feeds
M4	Named team: PM, key users, Accounting Manager, System Administrator, compliance officer, DPO	Sponsor	W1 for every size	Workshops, decisions
I1	Insurer list and agreements, commission and referrer rates, product list	Key users	W1 / W2 / W3 / W4	Configuration kit
I2	Chart of accounts and the	Accounting	W1 / W2 / W3 / W4	Configuration kit

ID	Input	Owner (broker)	Needed by: Small / Medium / Large / Enterprise	Feeds
	accountant's mapping decisions	Manager		
I3	User list with roles, branches and reporting lines (My Work > My Team follows the reporting line)	System Administrator	W1 / W2 / W3 / W3	Configuration kit, Users sheet
I4	SMTP mailbox and credentials	IT head	W1 / W2 / W2 / W2	E-mail test
I5	Bank accounts, one statement export per account, bank contacts, payee bank accounts	Accounting	W2 / W2 / W3 / W3	Statement formats, bank payment files
I6	Partner contracts and credentials (SMS provider, CTPL authentication provider, payment gateway, insurer API access)	IT head and sponsor	W2 / W3 / W4 / W6	Partner certifications
I7	COC number series of each insurer	Operations	W2 / W2 / W3 / W3	COC Series sheet, CTPL authentication
I8	Logo, sign-in picture, signatories with their e-signature consent	Marketing, signatories	W1 / W2 / W2 / W3	Branding, documents
G1	Extracts of clients, in-force policies, open items, open claims and the trial balance, cleansed	Data owners	W2 / W3 / W5 / W6	Mock load 1
I9	Training rooms, devices, attendance list	PM	Before end-user training	Training
I10	UAT testers and sign-off authority	PM	Before UAT	UAT

The insurer, product and commission data (I1) and the chart of accounts with its mapping (I2) are on the critical path for every size: the configuration kit cannot be completed without them, and everything after configuration waits for it. The user list (I3) has one to three days of float only.

5.2 The kits the inputs go into


The broker fills two workbooks downloaded from Master > Go-Live Data Load:

- the **configuration kit** (company, settings, PSGC regions, provinces, cities and barangays, branches, departments, hierarchy, designations, users, currencies, chart of accounts, banks, bank accounts, signatories, insurers, lines of business, products, covers, vehicles, suppliers, asset classes, short-period rates, cancellation reasons, claim document checklist, repair shops, commission rates, premium taxes, LGU rates, authority limits, numbering, payee bank accounts, COC series);
- the **migration kit** (clients, in-force policies, open items, open claims, opening balances), refused until the cutover date `golive.cutover_date` is set.

Each upload is validated as a trial run, the errors come back as an errors workbook, and a corrected file is loaded again without duplicates. A late or poor input therefore shows quickly as rows in error, which the project manager reports weekly.

6. Partner certifications

6.1 Partners and fallbacks

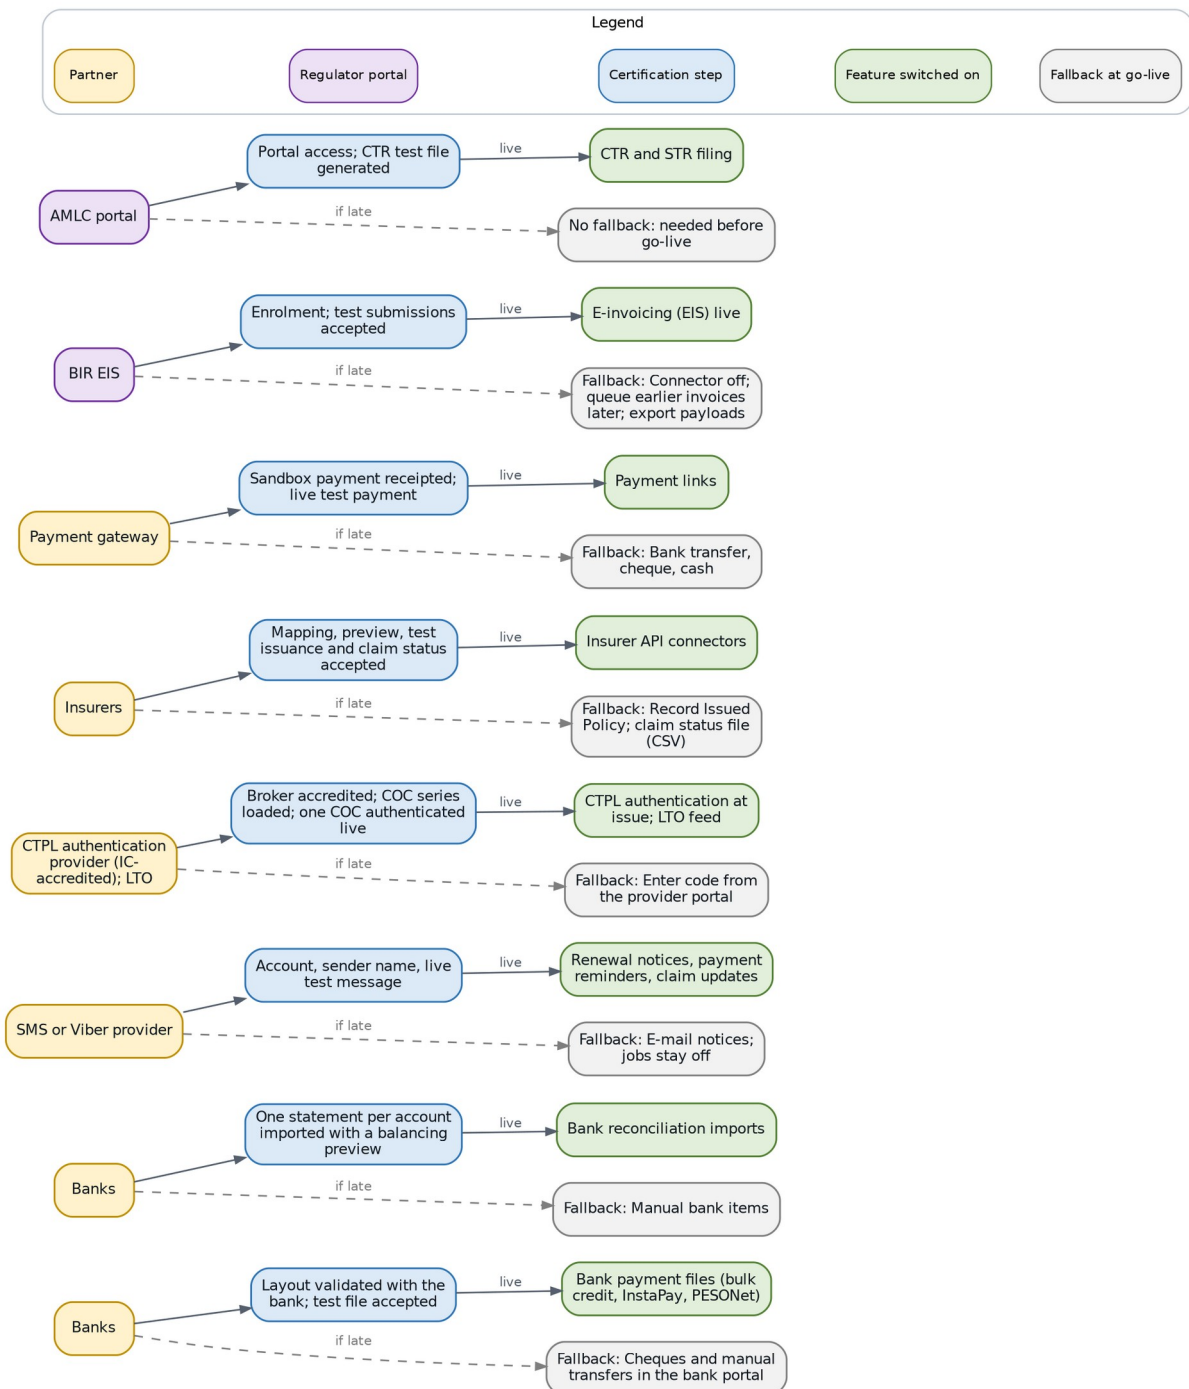

Partner certifications: what each partner certifies, the feature it switches on and the fallback while it is not certified

BrokerVerse delivers each connector in test mode (Master > System Configuration > Integrations): the whole process can be tried before the partner contract is signed. What is certified with each partner is done during onboarding with that partner; the system cannot certify it alone.

Partner	Certified during the project	Owner	Lead time assumption (S / M / L / E)	Fallback at go-live
Banks (payment files)	Each starter layout validated against the bank's current specification; a test file accepted by the bank	Bank, with Accounting	10 / 15 / 20 / 25 days	Cheques and manual transfers in the bank portal
Banks (statements)	One statement per account imported with a balancing preview	Accounting, with iorta TechNXT	3 / 4 / 6 / 8 days	Manual bank items
SMS or Viber provider	Account, sender name, live test message	Provider, with the IT head	5 / 8 / 10 / 10 days	E-mail notices; SMS jobs stay switched off
CTPL authentication provider (IC-accredited); LTO	Broker accredited; COC series loaded; one COC authenticated live; LTO feed when the provider does not send it	Provider, with Operations	8 / 10 / 15 / 15 days	Enter code from the provider portal on Operations > CTPL Authentication
Insurers	Mapping per insurer, preview, test issuance and claim status accepted	Each insurer, with the Processing Team	10 / 15 / 20 / 25 days	Record Issued Policy; claim status file (CSV)
Payment gateway	Sandbox payment receipted; one live test payment	Gateway, with Accounting	3 / 5 / 5 / 5 days	Bank transfer, cheque, cash
BIR EIS	Enrolment; test submissions accepted	Accounting Manager	30 days for every size	Connector off; Queue earlier invoices once live; Export payloads for a manual upload
AMLC portal	Portal access; a CTR test file generated	Compliance officer	15 / 20 / 20 / 20 days	None: needed before go-live

6.2 When each partner must be live

With the planned durations, every partner certification finishes before go-live except the EIS, which waits for the BIR enrolment and is switched on in the first hypercare week. The margin is the number of working days the certification can slip before the go-live starts with the fallback.


ID	Dependency	Small	Medium	Large	Enterprise
I6	Partner contracts and credentials	W1 to W2, 20 days before go-live	W1 to W3, 31 days before go-live	W2 to W4, 50 days before go-live	W2 to W6, 74 days before go-live
I7	COC series	W1 to W2, 24 days before go-live	W1 to W2, 36 days before go-live	W1 to W3, 59 days before go-live	W1 to W3, 89 days before go-live
N3	Bank payment files certified	W3 to W5, 8 days before go-live	W4 to W7, 11 days before go-live	W6 to W10, 21 days before go-live	W8 to W13, 39 days before go-live
N4	SMS or Viber live	W3 to W4, 13 days before go-live	W4 to W6, 18 days before go-live	W6 to W8, 31 days before go-live	W8 to W10, 54 days before go-live
N5	CTPL authentication live	W3 to W4, 10 days before go-live	W4 to W6, 16 days before go-live	W6 to W9, 26 days before go-live	W8 to W11, 49 days before go-live
N6	Insurer API connectors	W3 to W5, 6 days before go-live	W5 to W8, 9 days before go-live	W7 to W11, 19 days before go-live	W8 to W13, 37 days before go-live
N7	Payment gateway live	W3, 15 days before go-live	W4 to W5, 21 days before go-live	W6 to W7, 36 days before go-live	W8 to W9, 59 days before go-live
N8	EIS connector in	W4, 10 days	W7, 14 days	W10, 21 days	W13, 37 days

ID	Dependency	Small	Medium	Large	Enterprise
	test mode	before go-live	before go-live	before go-live	before go-live
N9	EIS connector live	W7, in the go-live week	W10, in the go-live week	W15, in the go-live week	W21, in the go-live week

CTPL authentication is the partner dependency with the most effect on daily work: every motor policy with CTPL needs an authenticated COC before release. If the provider is not live at go-live, the go/no-go records the decision to use **Enter code from the provider portal** for every COC, and Operations staff the extra work until the connector is live.

7. Regulatory registrations

7.1 What the broker registers, and what it unlocks

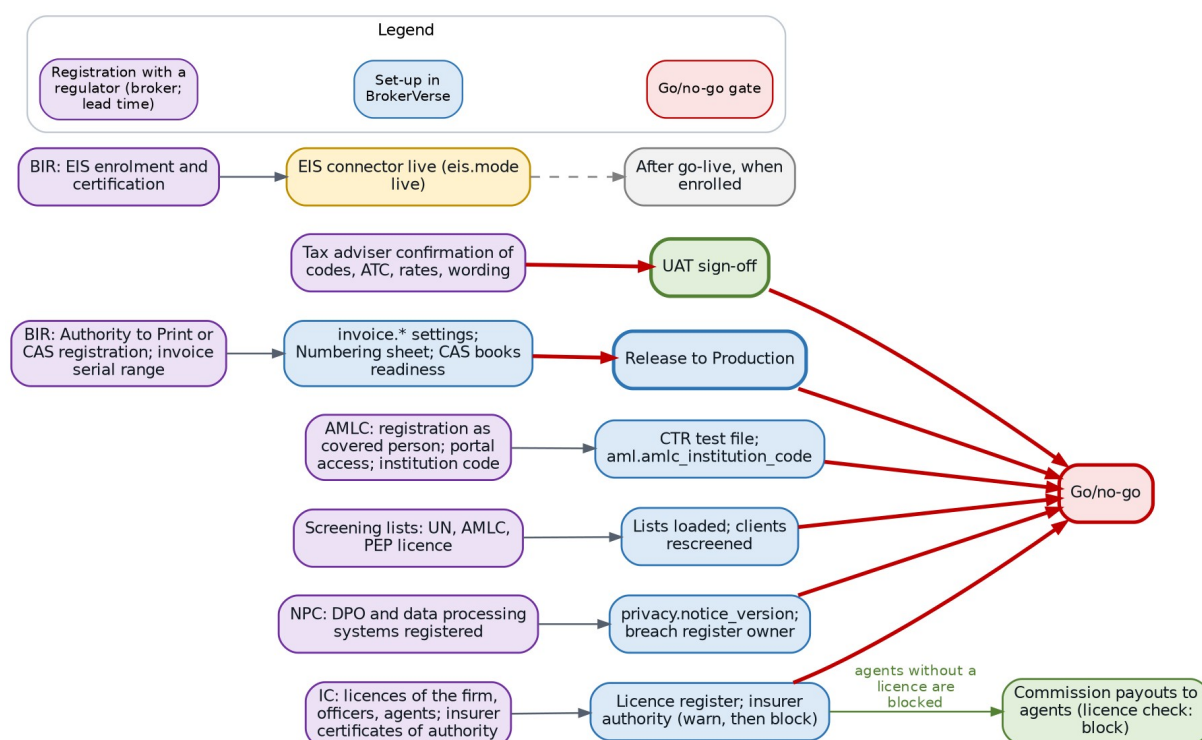

Regulatory registrations: the broker's registration with each regulator, its set-up in BrokerVerse and the gate it opens

The registrations are the broker's own obligations; iorta TechNXT plans around them and sets the system up from their results. A registration the broker already holds takes no lead time: it is confirmed at mobilisation and the task is closed.

ID	Registration	Owner	Lead time assumption (S / M / L / E)	Set-up in BrokerVerse	Gate
R1	BIR: Authority to Print or CAS registration; registered serial range of the sales invoices; last numbers used	Accounting Manager with the tax adviser	20 / 25 / 30 / 30 days	invoice.atp_number or invoice.cas_permit_number, invoice.serial_from, invoice.serial_to; Numbering sheet; CAS Books and Documents readiness (cas.permit_number)	Release to Production
R2	BIR: EIS enrolment and certification, when the broker is covered	Accounting Manager	30 days	eis.enabled, eis.mode, endpoint, accreditation id; credential variable names	Feature only
R3	AMLC: registration as covered person, portal access, institution code	Compliance officer	15 / 20 / 20 / 20 days	aml.amlc_institution_code, aml.amlc_transaction_codes; CTR test file	Go/no-go
R4	IC: licences of the firm, officers, licensed individuals and agents; certificates of authority of the insurers	Compliance officer	5 / 8 / 10 / 12 days	Compliance > Licence Register, Fit and Proper; insurer IC Certificate of Authority No. and validity	Compliance set-up; go/no-go


ID	Registration	Owner	Lead time assumption (S / M / L / E)	Set-up in BrokerVerse	Gate
R5	NPC: registration of the DPO and the data processing systems; privacy notice version	DPO	20 / 25 / 30 / 30 days	privacy.notice_version; breach register owner	Go/no-go
R6	Tax adviser confirmation of tax codes, ATC, rates, invoice and receipt wording, VAT treatment of commission	Tax adviser	5 / 5 / 8 / 10 days	Taxation, bir.*, invoice.*, receipts.document_title	UAT sign-off
R7	Screening lists: UN and AMLC lists obtained; PEP list licence from a provider when used	Compliance officer	10 / 12 / 15 / 15 days	Compliance > Screening Lists (no list content is delivered with BrokerVerse); aml.screening_provider	Go/no-go
R8	Written permission to use client marks, only with a client brand pack	Sponsor	3 / 5 / 5 / 5 days	Theme and Branding > Brand packs	Feature only

Points that matter to the plan:

- **ATP or CAS (R1)** is the regulatory item with the least float for a small broker: 2 working days. A broker that must register a new CAS or obtain a new ATP should start on the kick-off day, or the go-live moves.
- **Screening lists (R7)** must be loaded and every client screened before go-live: onboarding, policy issue and payouts check the lists, and a High-risk or matched client gets no policy. The UN and AMLC lists are public; a PEP list is licensed from a provider.
- **IC licence data (R4)** drives the commission payout check: with compliance.referrer_licence_check set to block (delivered), commission to an agent without a licence in force is refused. Load the licences before the first commission run after go-live.
- **Insurer certificates of authority** are checked at request for quotation, firm order and issue. Start with compliance.insurer_authority_check at warn (delivered) and switch to block once every insurer's certificate is entered.

8. Environments, pipeline and keys

8.1 Set-up order

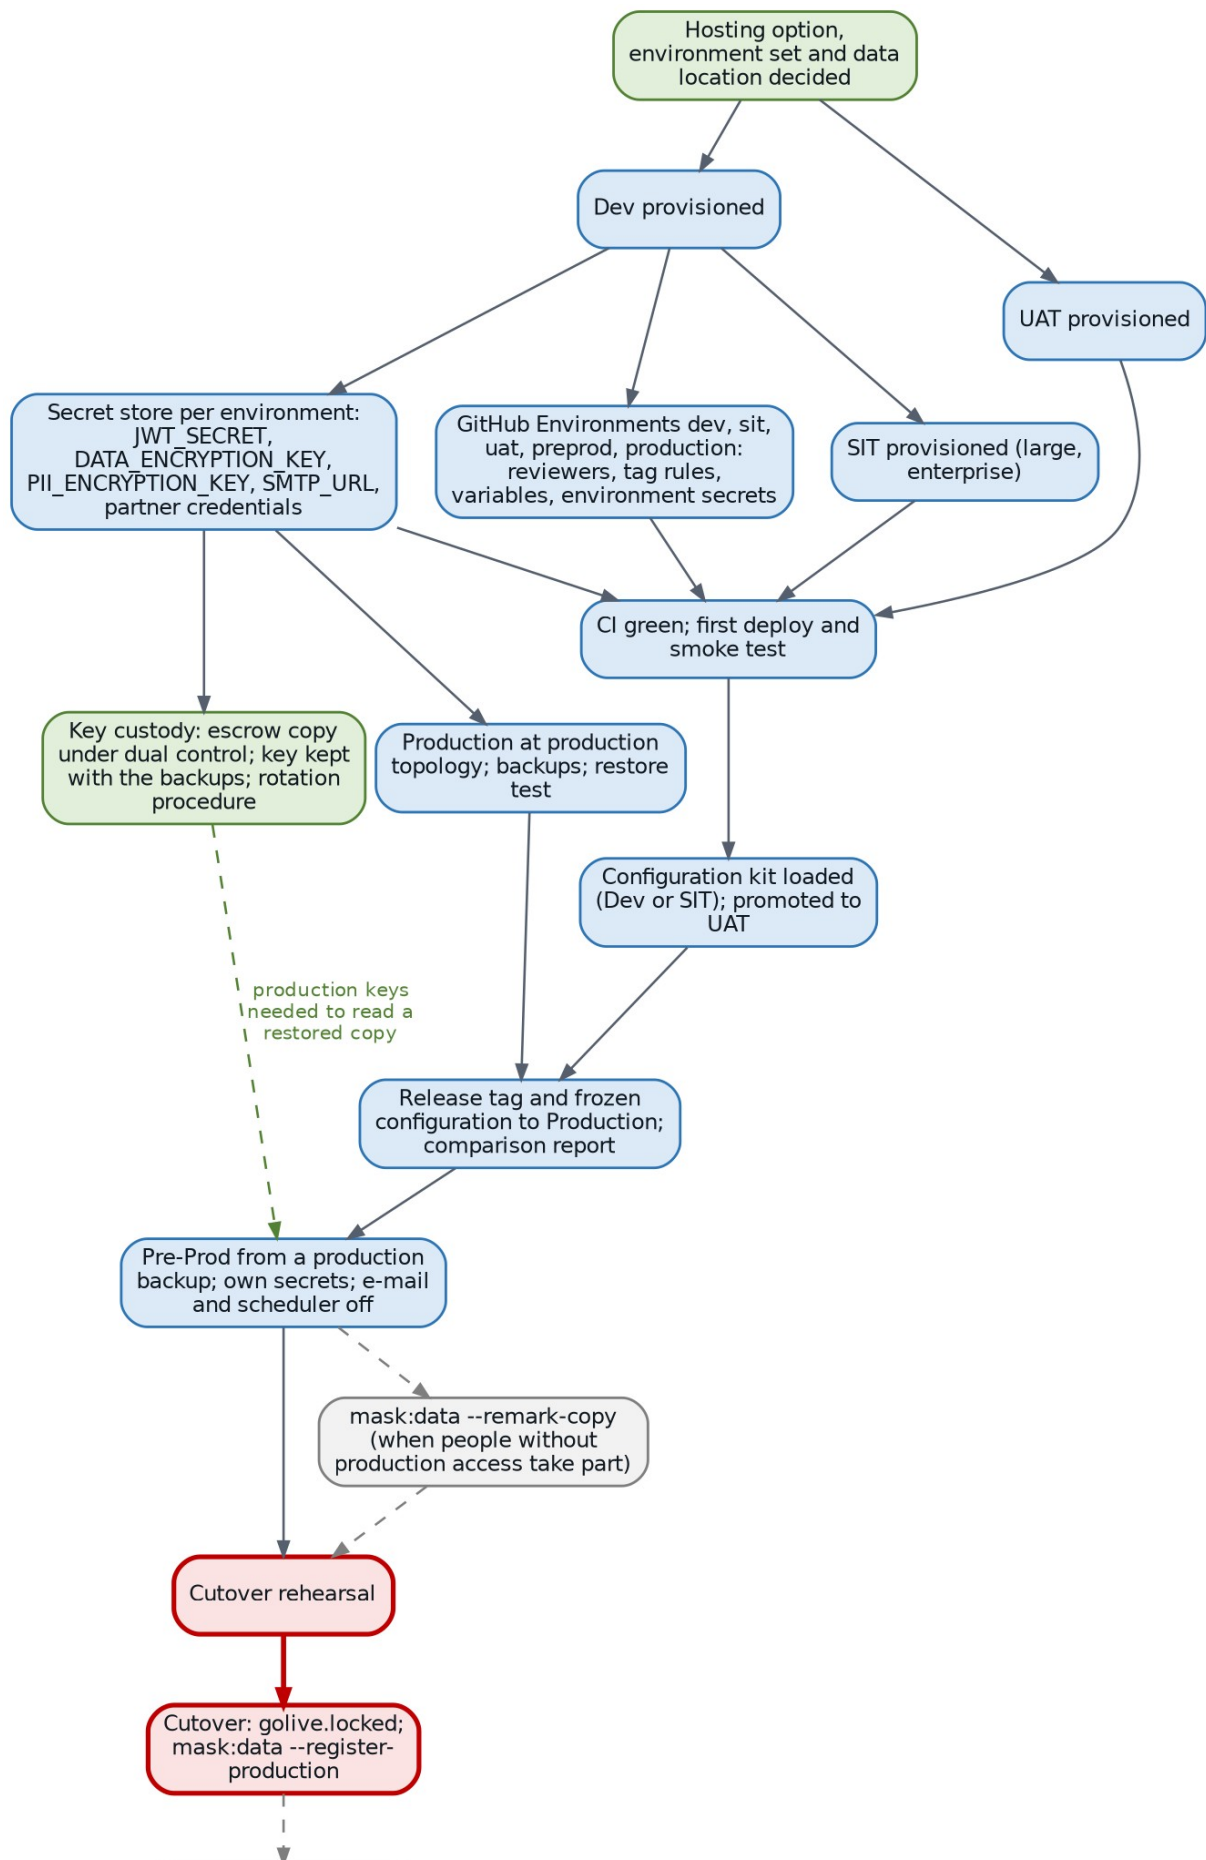

Environments, pipeline and encryption keys from the hosting decision to the removal of Pre-Prod

Environment set	Small and medium	Large	Enterprise
Standing environments	Dev, UAT, Production	Dev, SIT, UAT, Production with high availability	As large, with a cross-region copy of the backups
Where SIT runs	Dev (synthetic data only)	SIT	SIT
Mock loads	UAT	SIT, then UAT	SIT, then UAT
Pre-Prod	Temporary: created from a production backup for the rehearsal, removed after hypercare	Same	Same

ID	Step	Owner	Depends on	Float (S / M / L / E days)
M5	Hosting option, environment set and data location decided; transfer of personal data outside the Philippines decided and documented	Broker sponsor and IT head	Kick-off	4 / 8 / 12 / 17
E1, E2, E3	Dev, SIT (large, enterprise) and UAT provisioned	iorta TechNXT DevOps lead	M5	4 to 6 / 8 to 10 / 12 to 16 / 17 to 21
E4	GitHub Environments dev, sit, uat, preprod, production: required reviewers (two on production, prevent self-review), tag rules, variables (DEPLOY_ENABLED, targets, addresses) and environment secrets (deploy keys, known hosts, bucket and distribution ids)	iorta TechNXT DevOps lead	Dev	4 / 8 / 13 / 19
E5	Application secrets in the secret store of each environment: JWT_SECRET, DATA_ENCRYPTION_KEY, PII_ENCRYPTION_KEY (each at least 32 characters and different), SMTP_URL, partner credentials	iorta TechNXT DevOps lead with the broker IT head	Dev	5 / 9 / 14 / 20
E6	First deployment through the pipeline (CI green, deploy, smoke test) to Dev, SIT and UAT	iorta TechNXT DevOps lead	E3, E4, E5	4 / 8 / 12 / 17
E7	Production at production topology, backups, monitoring, restore test	iorta TechNXT DevOps lead	E5	13 / 23 / 42 / 67
X2	Pre-Prod from a production backup: own secrets, e-mail off, scheduler stopped; masked first when people without production access take part	iorta TechNXT DevOps lead; masking approved by the broker DPO	Release to Production	1 / 2 / 2 / 10
X5	Cutover: go live, locked switched on; npm run mask:data -- --register-production run once in Production	Broker System Administrator; iorta TechNXT DevOps lead	Go/no-go	0

8.2 Encryption key custody

PII_ENCRYPTION_KEY encrypts TIN, government ID numbers and bank account numbers at rest; DATA_ENCRYPTION_KEY encrypts two-step verification secrets. A

database backup cannot be read without the key it was written with. The key custody record is therefore a dependency of the first deployment, not a formality:

1. Each environment has its own keys; Production keys are generated in the production secret store and never leave it except as the escrow copy.
2. The escrow copy is kept under dual control (one person of the broker, one of iorta TechNXT, or as the hosting contract states), with the backups it opens.
3. Pre-Prod restored from a production backup needs the production keys to read the copy. After masking, the copy is rotated to its own key with the rotation procedure of `deploy/REFERENCE.md` (`npm run pii:rotate`).
4. A rotation keeps the previous key (`PII_ENCRYPTION_KEY_PREVIOUS`) until the dry run reports nothing left, and the old key is kept with the backups taken before the rotation.

If the custody record is not agreed, the first deployment can still go ahead in Dev with a development key, but Production is not provisioned (E7 depends on E5).

9. Critical path by size

9.1 How to read the charts


Each chart shows the chain of tasks with no float to the go-live, in rows of five from left to right. Blue boxes are iorta TechNXT tasks, green boxes broker tasks, red boxes the gates. A label on an arrow is a start-to-start link with its lag in working days (for example, SIT starts a number of days after on-screen configuration has started, not after it has finished).

The critical path is the same chain for every size, which is the main message for the project manager:

Client data for the configuration kit (insurers, rates, products, chart of accounts) > configuration kit filled and loaded > on-screen configuration > system integration test > promotion to UAT > UAT > cutover rehearsal > go/no-go > cutover > go-live.

Discovery workshops, environments and the regulatory registrations run beside it with some float; the size decides how much.


9.2 Small broker (8 weeks)

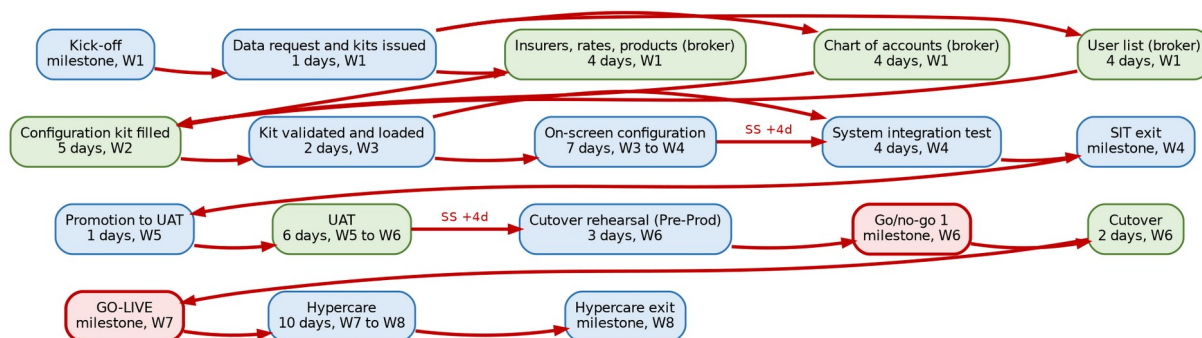

Critical path of a small broker

Item	Detail
Critical path	Kick-off (W1) > data request and kits issued (W1) > insurers, rates, products; chart of accounts; user list (W1) > configuration kit filled (W2) > kit loaded (W3) > on-screen configuration (W3 to W4) > SIT (W4) > SIT exit (W4) > promotion to UAT (W5) > UAT (W5 to W6) > cutover rehearsal (W6) > go/no-go (W6) > cutover (W6) > go-live (W7)
Near-critical (float 1 to 5 days)	Configuration complete, release to Production, Pre-Prod, UAT sign-off, train-the-trainer and end-user training 1 day; process workshops and BIR ATP or CAS 2 days; mock load 2 3 days; hosting decision, Dev, GitHub Environments, first deployment and compliance set-up 4 days; secrets and keys, fit-gap sign-off and branding 5 days
What it means	The small plan has almost no slack: 17 tasks are within one week of the critical path. Any input late by more than a week moves the go-live. Start the ATP or CAS request on the kick-off day


9.3 Medium broker (12 weeks)

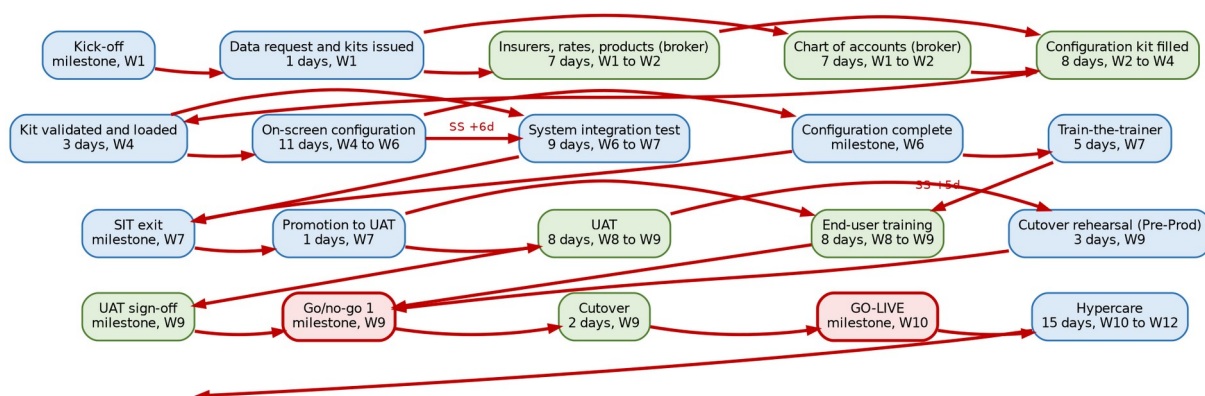

Critical path of a medium broker

Item	Detail
Critical path	Kick-off (W1) > data request and kits issued (W1) > insurers, rates, products and chart of accounts (W1 to W2) > configuration kit filled (W2 to W4) > kit loaded (W4) > on-screen configuration (W4 to W6) > SIT (W6 to W7) > SIT exit (W7) > promotion to UAT (W7) > UAT (W8 to W9) > cutover rehearsal (W9) > go/no-go (W9) > cutover (W9) > go-live (W10). A second critical chain runs through configuration complete (W6) > train-the-trainer (W7) > end-user training (W8 to W9)
Near-critical (float 1 to 5 days)	User list 1 day; release to Production and Pre-Prod 2 days; process workshops 3 days; compliance set-up 5 days
What it means	Training is as critical as testing: key users who are not released for train-the-trainer in week 7 move the go-live

9.4 Large broker (20 weeks)

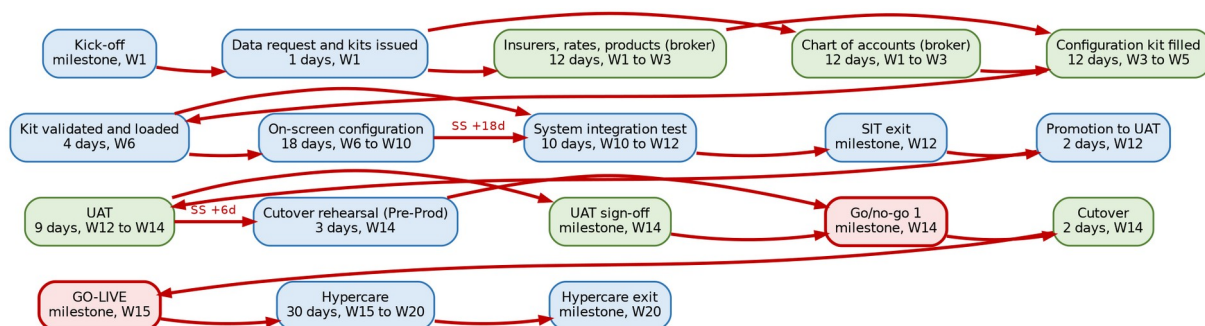


Critical path of a large broker

Item	Detail
Critical path	Kick-off (W1) > data request and kits issued (W1) > insurers, rates, products and chart of accounts (W1 to W3) > configuration kit filled (W3 to W5) > kit loaded in SIT (W6) > on-screen configuration (W6 to W10) > SIT (W10 to W12) > SIT exit (W12) > promotion to UAT (W12) > UAT (W12 to W14) > cutover rehearsal (W14) > go/no-go (W14) > cutover (W14) > go-live (W15)
Near-critical (float 1 to 5 days)	End-user training 1 day; user list, release to Production, Pre-Prod and mock load 3 2 days; configuration complete and train-the-trainer 5 days

Item	Detail
What it means	Mock load 3 in UAT has 2 days of float: a poor second mock load in SIT moves the go-live. Branch training must finish in week 14

9.5 Enterprise broker (26 weeks)

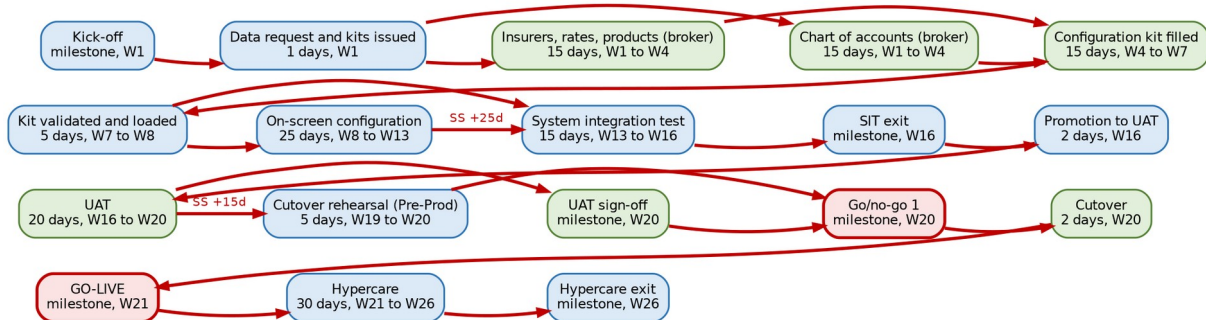

Critical path of an enterprise broker

Item	Detail
Critical path	Kick-off (W1) > data request and kits issued (W1) > insurers, rates, products and chart of accounts (W1 to W4) > configuration kit filled (W4 to W7) > kit loaded in SIT (W7 to W8) > on-screen configuration (W8 to W13) > SIT (W13 to W16) > SIT exit (W16) > promotion to UAT (W16) > UAT (W16 to W20) > cutover rehearsal (W19 to W20) > go/no-go (W20) > cutover (W20) > go-live (W21)
Near-critical (float 1 to 5 days)	User list 3 days; mock loads 3 and 4 and end-user training 5 days
What it means	The registrations have weeks of float; the risk sits in the volume of the configuration (more lines of business, insurers and products) and in four mock loads before the rehearsal

10. Lead times

ID	Item	Owner	Small	Medium	Large	Enterprise
R1	BIR ATP or CAS, invoice serials	Broker Accounting Manager with the tax adviser	20 days	25 days	30 days	30 days
R2	BIR EIS enrolment	Broker Accounting Manager	30 days	30 days	30 days	30 days
R3	AMLC registration	Broker compliance officer	15 days	20 days	20 days	20 days
R4	IC licence data	Broker compliance officer	5 days	8 days	10 days	12 days
R5	NPC registration	Broker DPO	20 days	25 days	30 days	30 days
R6	Tax adviser confirmation	Broker tax adviser	5 days	5 days	8 days	10 days
R7	Screening lists and licence	Broker compliance officer	10 days	12 days	15 days	15 days
R8	Permission for client marks	Broker sponsor	3 days	5 days	5 days	5 days
I6	Partner contracts and credentials	Broker IT head and sponsor	8 days	10 days	15 days	20 days
N3	Bank payment files certified	Bank, with Accounting and iorta TechNXT	10 days	15 days	20 days	25 days
N4	SMS or Viber live	SMS provider, with the broker IT head	5 days	8 days	10 days	10 days
N5	CTPL authentication live	IC-accredited authentication provider, with Operations	8 days	10 days	15 days	15 days
N6	Insurer API connectors	Insurers, with the Processing Team	10 days	15 days	20 days	25 days
N7	Payment gateway live	Payment gateway, with Accounting	3 days	5 days	5 days	5 days
E7	Production provisioned	iorta TechNXT DevOps lead	5 days	8 days	10 days	12 days
G1	Extraction and cleansing	Broker data owners	8 days	12 days	20 days	25 days

The lead times of the BIR, the AMLC, the NPC and the IC are assumptions, not commitments of those agencies. Ask the broker at mobilisation which registrations it already holds, which are in progress and their reference numbers, and record each one as a dependency in the RAID log with its expected date.

11. What slips if a dependency slips

11.1 Dependencies that hold the go-live

The table gives the float to go-live in working days. A dependency that finishes N days late moves the go-live by N less its float (never less than zero). A float of 0 moves the go-live day for day.

ID	Dependency	Small	Medium	Large	Enterprise
M4	Broker team named	10	14	24	30
M5	Hosting and environment set decided	4	8	12	17
E1	Dev provisioned	4	8	12	17
E2	SIT provisioned	n/a	n/a	12	17
E3	UAT provisioned	6	10	16	21
E4	GitHub Environments set up	4	8	13	19
E5	Secrets and encryption keys	5	9	14	20
E6	First pipeline deployment	4	8	12	17
E7	Production provisioned	13	23	42	67
D1	Process workshops	2	3	7	6
D2	Compliance workshop	10	15	24	30
I1	Insurers, rates, products	0 (critical)	0 (critical)	0 (critical)	0 (critical)
I2	Chart of accounts	0 (critical)	0 (critical)	0 (critical)	0 (critical)
I3	User list and reporting lines	0 (critical)	1	2	3
I4	SMTP mailbox	23	36	60	90
I5	Bank accounts and statement samples	19	30	51	77
I8	Logo, pictures, signatories	12	18	38	54
I9	Training rooms and attendees	17	28	52	75
I10	UAT testers named	18	31	53	72
R1	BIR ATP or CAS, invoice serials	2	12	31	58
R3	AMLC registration	12	22	46	76
R4	IC licence data	10	14	31	48
R5	NPC registration	8	18	38	68
R6	Tax adviser confirmation	8	14	23	42
R7	Screening lists and licence	15	26	47	76
C1	Configuration kit filled	0 (critical)	0 (critical)	0 (critical)	0 (critical)
C2	Configuration kit loaded	0 (critical)	0 (critical)	0 (critical)	0 (critical)
C3	On-screen configuration	0 (critical)	0 (critical)	0 (critical)	0 (critical)
K1	Compliance set-up	4	5	15	27
K2	Screening lists loaded	11	17	30	51
K3	AMLC report file test	11	17	29	50
B1	Branding and brand pack	5	7	18	31
N1	E-mail tested	21	34	53	82
N2	Bank statement imports	13	20	33	54
G1	Extraction and cleansing	10	20	31	47
G2	Mapping to the migration kit	12	22	35	52
G3	Mock load 1	6	13	23	37
G4	Mock load 2	3	7	10	17
G5	Mock load 3	n/a	n/a	2	5
G6	Mock load 4	n/a	n/a	n/a	5
L1	Train-the-trainer	1	0 (critical)	5	12
L2	Compliance officer and DPO training	11	17	29	50
L3	End-user training	1	0 (critical)	1	5
T1	System integration test	0 (critical)	0 (critical)	0 (critical)	0 (critical)
T4	UAT	0 (critical)	0 (critical)	0 (critical)	0 (critical)
X1	Release to Production	1	2	2	10
X3	Cutover rehearsal	0 (critical)	0 (critical)	0 (critical)	0 (critical)

11.2 What else moves with it

Dependency late	Tasks that move with it	Effect beyond the date
Insurers, rates, products; chart of accounts (I1, I2)	Configuration kit, every task after configuration	Day for day on the go-live; the mock loads cannot reconcile commission and the ledger without them
User list (I3)	Configuration kit load; training users	My Work > My Team and the approval routing follow the reporting line: a late or wrong hierarchy shows in UAT as misrouted approvals
Discovery decisions (D1)	Fit-gap sign-off; on-screen configuration	Rework of the Product Configurator if acceptance rules or rating factors change after build
Hosting decision, environments, keys (M5, E1 to E6)	Configuration kit load, then the critical path	Without the key custody record Production is not provisioned
BIR ATP or CAS (R1)	Release to Production, Pre-Prod, rehearsal	Invoices and receipts cannot be issued from BrokerVerse at go-live; a go-live with manual invoices under the old ATP needs the tax adviser's written agreement
AMLC registration (R3)	AMLC report file test, go/no-go	Covered transactions cannot be filed within 5 working days (aml.ctr_due_working_days)
Screening lists (R7, K2)	Go/no-go	Clients are not screened at onboarding and issue; the compliance officer cannot sign the go/no-go
IC licence data (R4)	Compliance set-up	Commission payouts to agents are refused (licence check block) until the licences are entered
NPC registration (R5)	Go/no-go	The broker processes personal data in a new system without its registration updated; the DPO decides
Tax adviser confirmation (R6)	UAT sign-off	VAT, withholding and invoice wording are not accepted; the BIR forms of the first month are at risk
Mock loads (G3 to G6)	Later mock loads, rehearsal	Data quality found late; the rehearsal is the last chance to reconcile
Training (L1, L3)	Go/no-go	Users without an assessment do not receive production access
UAT (T4)	Sign-off, go/no-go, payment milestone	Day for day; the UAT sign-off payment milestone moves with it

11.3 Feature-only dependencies

Dependency late	The go-live holds; meanwhile	Switched on when
Bank payment files (N3)	Cheques and manual transfers in the bank portal	The bank accepts the test file
SMS or Viber (N4)	E-mail notices; jobs sms-renewal-notices and sms-payment-reminders	The connector is live and a test message is sent

Dependency late	The go-live holds; meanwhile	Switched on when
	stay off	
CTPL authentication (N5)	Enter code from the provider portal for each COC	One COC is authenticated live
Insurer APIs (N6)	Record Issued Policy ; claim status file	Each insurer accepts the test requests; insurer by insurer
Payment gateway (N7)	Bank transfer, cheque, cash	A live test payment is receipted
BIR EIS (R2, N8, N9)	Connector off; invoices issued and kept	Enrolment; then Queue earlier invoices sends the invoices issued since go-live
Client brand pack (R8, B2)	The broker's own theme or the delivered preset	Written permission is on file

12. Managing the dependencies

1. **At mobilisation**, the project manager walks this map with the broker: which registrations are held, which partners are contracted, who owns each input. Every dependency becomes a D line of the RAID log with its owner, needed-by week and state.
2. **Every week**, the status report lists the dependencies due in the next two weeks and those At risk or Late. A dependency with float of 5 days or less is reported even when on track.
3. **Escalation**: a dependency on the critical path late by 3 working days, or any dependency late by more than its float, goes to the steering committee with the effect on the go-live from the tables above.
4. **Re-baseline**: when a dependency moves the go-live, the steering committee agrees the new date; the plan workbook is rebuilt from the model with the new durations, and the change is recorded under the change control of the Statement of Work.
5. **At go/no-go**, the feature-only dependencies still open are listed with their fallback and the date the feature is expected; the go-live communication tells users which fallback they use.

13. Document Sign-Off

Serial Number	Description	Owner	Status
1	No open items at the time of issue	iorta TechNXT	

Sign Off Date	Signature	Approved By	Department & Project Role



Insurance technology for the Philippines



10+

COUNTRIES

Global Presence



8

GLOBAL OFFICES

Strategically Located



11+

MARKETS SERVED

Across Continents



100%

COMMITMENT

To Excellence



MALAYSIA



INDIA



PHILIPPINES



THAILAND



VIETNAM



USA



ETHIOPIA



CAMBODIA



HONGKONG



SINGAPORE



Scan More Details
